

AIM

AP.020 PROJECT TEAM ORIENTATION PLAN

<Company Long Name>

<Subject>

Author: <Author>
Creation Date: February 12, 1999
Last Updated: August 15, 2025
Document Ref: <Document Reference Number>
Version: DRAFT 1A

Approvals:

<Approver 1>

<Approver 2>

ORACLE®

Copy Number _____

Document Control

Change Record

Date	Author	Version	Change Reference
12-Feb-99	<Author>	Draft 1a	No Previous Document

Reviewers

Name	Position

Distribution

Copy No.	Name	Location
1	Library Master	Project Library
2		Project Manager
3		
4		

Note To Holders:

If you receive an electronic copy of this document and print it out, please write your name on the equivalent of the cover page, for document control purposes.

If you receive a hard copy of this document, please write your name on the front cover, for document control purposes.

Contents

Document Control	ii
Introduction	1
Purpose	1
Overview	1
Session Overview	1
Project Team Induction	6
Executive Project Strategy	6
Charters and Roles	6
Stakeholder Analysis	6
Sponsorship Profile and Authority	7
Application Overview	8
Cross-Functional Team Dynamics	8
Application Overview	9
Impact and Risk Assessment	10
Cross-Functional Decision Making Setup	11
Decision Making/Problem Solving Model	11
Team's Decision Making Approach	11
Rules of Engagement	13
Operating Norms	13
Implementation Team Support Requirements	14
Change Leadership Guiding Principles and Roles	15
Reactions to Change	15
Change Model	15
Guiding Principles for Effective Change	16
Change Leadership Behaviors	16
Induction Checklist	20
Open and Closed Issues for this Deliverable	21
Open Issues	21
Closed Issues	21
Appendix A - Implementation Team Interview Guide	22
Implementation Team Insights Interview Questions	22
Appendix B - Project Team Performance Measures	24
Rules of Effective Metrics Program	24

Approach 24

Project Metrics..... 24

Project Team Performance Tracking 25

Introduction

Purpose

The purpose of this document is to assist the project team in successfully defining and refining the project mandate for which it is accountable. The decisions related to the mandate of the <Project Name> were captured as the refined Executive Project Strategy (AP.010). Further, the project team refined the practices for successful management of its mandate, and learned about its role as change leaders. The decisions related to the detailed management of the project for <Project Name> are captured in the Project Management deliverables.

Overview

This document includes the following components:

Components	Description
Introduction	Shows the outline for the work session.
Current Project Team Induction	Exposes the current members of the team to the mandate delegated to them by the steering committee. Included here is the review of the vision, benefits, expected results, alignment with Information Technology and corporate strategy, steering committee roles and performance measures, charter (including roles and performance measures) for the project team, and finally, the decisions, made or to be made, on the implementation strategy and project environment.
Application Overview	Positions the application potential within the context of the key project decisions.
Cross-Functional Decision Making Set-Up	Highlights the dynamics of cross-functional team work, applicable to the implementation team.
Rules of Engagement	Highlights the project team members' group operating norms.
Change Leadership Guiding Principles and Roles	Describes the guiding principles of change and highlights the role of the project team members as change leaders.
Induction Checklist	Lists the recommended steps to bring any new member on the project team.
Appendix A	Implementation Team Interview Guide
Appendix B	Sample project team performance measures

Session Overview

Purpose

This project team initial orientation session assembled the current members to expose them to the mandate delegated to them, and to help them understand the Executive Project Strategy initiated by the executives and the steering committee. As a result of the session, the project team could build on the initial project decisions and became ready to commit to the project.

The current members of the project team fine-tuned their rules of engagement. A module dedicated to effective change leadership guided a discussion on how the

project team members would fulfill their role as change leaders within the organization.

The orientation session was highly interactive and focused on decision making around key questions to help the project team engages in a successful charter for itself:

- Why we are going ahead with this project? What the business drivers leading the project are?
- What the expectations for the project and the project team members are?
- What the terms of reference for the project are?
- How the charter of the project team and the charter of the steering committee complement one another seamlessly?
- How the project team members interact together?
- What decisions are made, by whom? What are the authority levels?
- Who owns which action? When will the action be started? Completed? What are the dependencies?
- How the project team reports back to the steering committee?
- What practices the team adopts as rules of engagement?

The orientation session looked at ways of answering these questions and examined the project issues relevant to the launch of the project team and a successful completion of the project.

Facilitation

The work session was facilitated by <Facilitator Name> from

<Facilitator Name> Biographical Notes:

In addition, <Scribe's Name> attended the session to keep a record of all decisions made during the meeting and keep deliverables updated at all times throughout the session.

Attendees

The following people attended the initial project team orientation:

Organization	Name of Attendees	Title
<Company Long Name>		
Contract Resources		

Outline of the Session

The following outlines the event conducted for the orientation session.

Sections	Description	Time	Duration
CURRENT PROJECT TEAM INDUCTION			
Introduction Give background for the decision to go ahead with the project Introduce and welcome project manager and leads, including in each introduction, a brief statement of why the person is chosen. Make the point that the participants will in turn facilitate a similar induction session with their project team members. Describe the benefits of the project to the organization, the project team as a whole, and to the individuals who are a part of the team Express (the executive sponsor's) own commitment to making the project a success	Overview of the session: purpose, expectations, logistics, etc.		¼ hour
Implementation Model (See Implementation Model component in the Executive Project Strategy, AP.010) Review guidelines for successful application implementation and most common causes of failure	Highlights the model for successful application implementations; this model guides the refinement of the strategy for the project <Project Name>.		¼ hour
Executive Project Strategy Review vision, benefits, expected results (objectives and measures) Review the project alignment with Information Technology and corporate strategy Discuss high-level view of the impact of the project on technology, process and people Outline risks associated with the project Review the key project implementation decisions and their rationale Review executive decisions already made	Provides opportunity for project team to refine the executive thinking behind the Executive Project Strategy. Confirms the importance of the project for the organization.		1 ½ hours
Charters and Roles Review charter for steering committee Review list of steering committee members and their roles Explain levels of decision making and accountability Describe interaction of the steering committee and the project team Present and refine the project team charter and the division of responsibilities between the steering committee and the project team Discuss performance expectations, responsibilities and accountabilities of the project team	Provides the forum for the project team to refine its charter and clarify the project team role(s) and those of the steering committee.		½ hour
Stakeholder Analysis Refine Stakeholder Analysis List anticipated reactions, potential issues and prioritize List specific benefits to gain buy-in	Brings to the forefront the list of groups impacted (directly and indirectly) by the project. Validates the executive analysis and adds project team's input on stakeholder analysis.		½ hour

Sections	Description	Time	Duration
Sponsorship Profile and Authority Discuss characteristics and functions of effective sponsors Compare validated stakeholder map to Sponsor Profile Matrix and refine Agree on project team own sponsorship responsibilities Stress importance of long-term commitment and involvement essential to project's success	Furthers the development of the sponsorship network, to include the project team sponsorship responsibilities.		½ hour
Conclusion Review any logistics pertinent to the team Summarize information about alignment between corporate vision, business objectives and project vision Recount benefits on all levels Announce next work session(s)	Confirms appreciation to the project team for taking on the responsibility and restates promise of support and commitment for the duration of the project.		½ hour
APPLICATION OVERVIEW			
Introduction Position the context of defining cross-functional dynamics for the project team Review rest of agenda: Application Overview, Review of, Impact/Risk Assessment	Overview of the session: purpose, expectations, logistics, etc.		¼ hour
Cross-Functional Team Dynamics Define "team"; contrast work teams and project teams Describe characteristic of high-performance teams Identify challenges of cross-functional teams Identify stages of team development Discuss danger signs	Develops the individual and group skill sets to work efficiently and perform as a team		4 hours
Application Overview Structure Functionality Information flows On-line demo	Gives project team members the overview they need to understand and plan for the ramifications of the implementation decisions.		8 hours per Application Suite
Impact Assessment For each critical implementation decision, determine level of impact on technology, process and people Analyze the consequences of the impact	Gives a realistic picture of the technology-driven change and prepares for proactive management of the consequences of the system implementation.		3 hours
Risk Assessment Identify risks and barriers and determine actions to mitigate risks/barriers	Highlights the risks that might impair success and generates the action items that are needed to mitigate those risks, to be added to the project plan.		2 hours
Project Implementation Decisions Consolidate the action items identified to manage the impact and the risks associated with the critical implementation decisions Develop resource projection	Validates the action items developed in the session and favors congruity.		1 hour
CROSS-FUNCTIONAL DECISION MAKING SET-UP			
Introduction Position the context of identifying decision making norms for the project team	Overview of the session: purpose, expectations, logistics, etc.		¼ hour

Sections	Description	Time	Duration
Cross-Functional Decision Making Model Facilitate the Desert Survival or Jungle Survival activity Present basic decision making model Identify effective alternatives for generating options Discuss possible approaches to decision making Decide who will make decisions, what decisions they have the authority to make, what constraints are in place Select approach for the project team, to be initially applied	Allows the team to define the detail of their decision making approach, using a fictitious example first, to prepare them to the upcoming AIM planning session.		1 hour
AIM Planning Determine what resources and tasks will be executed if not explicitly stated in contract with the organization.	Customizes the AIM tasks and deliverables, along with resource requirements, to the customer-specific needs. Provides a forum for the project team members to use the decision making approach they agreed to in the previous work session.		Up to 5 days
RULES OF ENGAGEMENT			
Define procedures around all relevant areas of project management Agree on communication standards and model for the project team Define project team group operating norms	Highlights decisions (short and long term) around project management practices, including the team's internal communication practices.		4-6 hours
CHANGE LEADERSHIP GUIDING PRINCIPLES AND ROLES			
Review examples of recent change and reactions to those changes Discuss guiding principles for effective change leadership Agree on roles of project team members as change leads	Highlights the 8 guiding principles to effective change leadership, describes the typical reactions to change and guides the discussion on the roles of the project team members as change leaders		2 hours
INDUCTION CHECKLIST			
Create a list of steps required for new team member induction	Highlights the approach and actions to facilitate the induction of a new member to the team.		1 hour

Project Team Induction

Executive Project Strategy

We discussed the following from the Executive Project Strategy (AP.010):

- Background for the decision to go ahead with the project.
- Why each member was chosen.
- Benefits of the project to the organization, the project team as a whole, and to the individual leads and members.
- Implementation Guidelines for a successful application implementation project.
- Project vision and expected results (objectives and measures).
- Alignment of project vision with Information Technology and corporate strategy.
- High level impact of the project on the organization's current technology, processes and people.
- Key project implementation decisions and their rationale
- High level risks associated with the project (for example, the impact of significant delays).
- Other executive decisions, already made.

Charters and Roles

We reviewed the following from the Executive Project Strategy (AP.010):

- Charter for steering committee
- List of steering committee members and roles
- Levels of decision making and authority established for the steering committee and the project team
- Project team charter and the division of responsibilities between the steering committee and the project team
- Performance expectations and the responsibilities of the project team
- Response time to the project team for critical decisions to be made by the steering committee

Stakeholder Analysis

The following represents the analysis of our stakeholder constituencies:

-
-
-

Sponsorship Profile and Authority

Specific project team members' sponsorship responsibilities include:

- Communicate positively and frequently about the project to the people with whom they come into contact
- Be supportive of the people assigned to the project and remove barriers for the people in their sub-teams
- Maintain commitment in themselves for the project throughout its lifecycle
- Use resources wisely
- Keep executive sponsor alerted of danger signals early enough so dangers can be avoided
-

Application Overview

Cross-Functional Team Dynamics

Definition of a High Performance Cross-Functional Team

Cross-functional team applies to ...

Project teams differ from work teams in that ...

The characteristics of a high-performance cross-functional team are:

- common goals
- shared responsibility
- shared risks
- willingness to learn
- ability to have fun
- reliability
- interdependence
- effective communication
- high skill levels
- participative leadership
-

Challenges Inherent to a Cross-Functional Team

The major challenges of our cross-functional team will be:

- establishing identity/cohesion
- building interdependence
- coping with different cultural pressures
- dealing with geographical separation
- working through hierarchical issues
- establishing role clarity
- developing communication skills
- dealing with team life span and closure
- leadership responsibilities
- sponsorship responsibilities

The Stages of Team Development

A team typically goes through the following stages of development:

Stages of Development (Tuckman's Model)	Measures to Move on to the Next Stage
Forming	
Storming	
Norming	
Performing	

Danger Signs

Typically, the team should be alert to the following danger signs:

Danger Signs	Measures to Mitigate

Application Overview

Application Overview Modules

The modules included in the Application Overview are:

Topics

The topics covered in the Application Overview are:

- Overview
- Introduction to Applications
 - Start-up and log on to Applications
 - Navigate through the system
 - Assign values to common profile options
- Applications Structures
 - Review the basic structures on which the applications are built
 - Discuss system administrator functions such as defining a user and building Alerts
- Application Functionality
 - Review the functionality of each application
 - Identify the dependencies between applications
 - Compare data that is shared between different applications, such as customers, suppliers and accounting information.
- Follow the Information Flows Between Applications

- Review the use of open interfaces which allow Applications to receive data from external sources
- View on-line demonstration of Applications

Impact and Risk Assessment

The following are the major impact, risks and barriers, and action items discussed by the group:

Cross-Functional Decision Making Setup

Decision Making/Problem Solving Model

The following is the decision making/problem solving model agreed to by the project team:

#	Step	Notes
1	Define (Opportunity or Problem)	- Who/Who not? - Where/Where not? - When/When not? -
2	Identify Probable Causes	Use the 5 why's
3	Develop Courses of Actions/ Alternatives	Divergent vs. Convergent thinking cover all bases – no holes or gaps, also develop contingency plan
4	Chose Options	Nominal grouping, consensus, voting, affinity diagram, let one person decide, dice, easy out, spell out, best home or balance sheet
5	Implement	Implement the solution – determine strategy to implement
6	Observe and Evaluate	Track solution implementation: Did it allow to meet the objective (or solve the problem)? If not, go back to Step 1. Refine as necessary.
7	Celebrate/Closure	Celebrate and congratulate, then move on.

Effective Techniques to Tap Into Creativity

The following techniques were reviewed for the team:

- Brainstorming
- Nominal
- Group
- Plus/Minus/Interesting
- Random Simulation
- Escape Method
- Synergistics
- ...

Team's Decision Making Approach

The project team agreed to the following approach for decision making:

Types of Decision	People to Involve	Empowered Yes or No	Need Approval Yes or No	Approach	Criteria
Routine					
Resourcing					

Types of Decision	People to Involve	Empowered Yes or No	Need Approval Yes or No	Approach	Criteria
Scope					
Facilities					

Rules of Engagement

Operating Norms

Checklist of Group Operating Norms

Typical group norms include the following:

- Agree to **share responsibility** for making the group work by taking **initiative** in starting and contributing to interaction.
- Speak only when no one else is speaking.
- Do **not interrupt**.
- **Listen** to understand rather than to rebut.
- **Honor time boundaries** – start times, stop times, due dates, ...
- **Disclose** your thoughts and feelings about the group process,
- **Be objective**, suggestions should facilitate solutions, not point blame.
- Say what you think and feel **in** the team meeting rather than saving it for discussion outside the team with only some of the team members.
- Deal with the **here-and-now** rather than focusing on history and incidents outside the team.
- Speak **to** individuals in the team rather than talking about them, when they are present or absent.
- Offer **support** to others.
- Offer helpful **confrontation** to others.
- Explore your **reactions** when confronted.
- **Express** reactions to the interactions of others.
- Speak for **yourself**. Do not generalize without substantiation.
- Be concrete and **specific** in your observations.
- Deal **directly** with conflict and differences.
- Acknowledge your appreciation for **feedback**.
- **Avoid** advising, interpreting, premature problem-solving, labeling/diagnosing, personalizing.
- Demonstrate **initiative** by participating in discussion, completing assignments, and looking for ways to improve processes.
- **Address conflict**, competition, and conflict avoidance **openly**.
- Seek an agreeable, **workable solution jointly**.
- Treat team members with **respect** and support.
- Use concrete, **specific examples**.

- Maintain **confidentiality**.

Project Team Norms and Behaviors

Our team will adhere to the following:

Norms	Corresponding Behaviors	Measures in case of non-compliance

Implementation Team Support Requirements

Consider the following when deciding how to extend technical support to the implementation team:


- training the help desk
- Technical Assistance Request (TAR) resolution procedure
- apprenticeships
- list of hardware and software requirements
- procurement of hardware and software
- installation of hardware and software
- testing environment
- learning environment
- internal service level agreements
- external service level agreements
- support of web site and/or repository
- problem resolution procedure
- upgrades or patches for software
- DBA training (starting the learning events for the DBA now can give the person a chance to get involved and learn throughout the implementation)
- passing lessons learned from implementation to help desk
- installation failure policy
- lines of delineation for budget responsibility, for example, are the business units or the Information Technology department paying for the learning events for the implementation team

Change Leadership Guiding Principles and Roles

Reactions to Change

Accelerating the Path Through the Valley of Despair


As users react to change through shock, fear and “wait and see” attitude before they commit to the new roles they must fulfill, there is a great drop in productivity. Adoption tasks aim at accelerating the cycle of reaction to change so the productivity drop is lessened and users achieve acceptance faster and generate higher productivity.

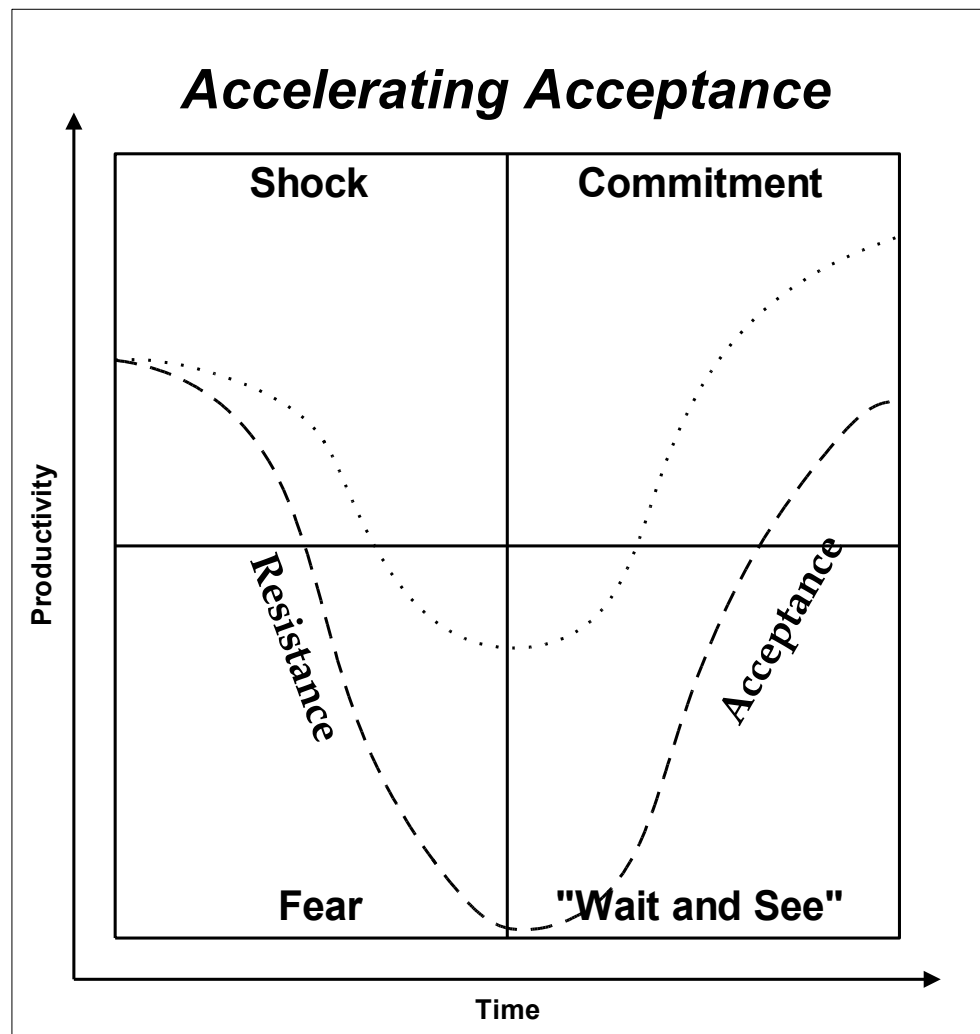

Change Model

To Change, Individuals Need the Will and the Abilities


To facilitate the change from the present to the desired situation, users need the will and the abilities to change.

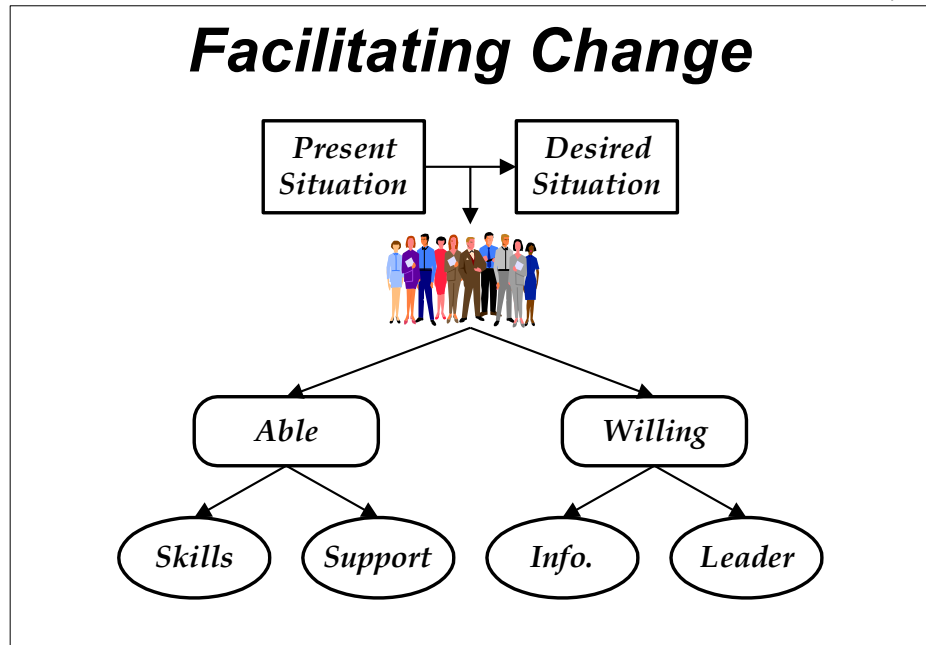

Guiding Principles for Effective Change

Leading Change From Resistance to Resilience

There are eight guiding principles for effective change.

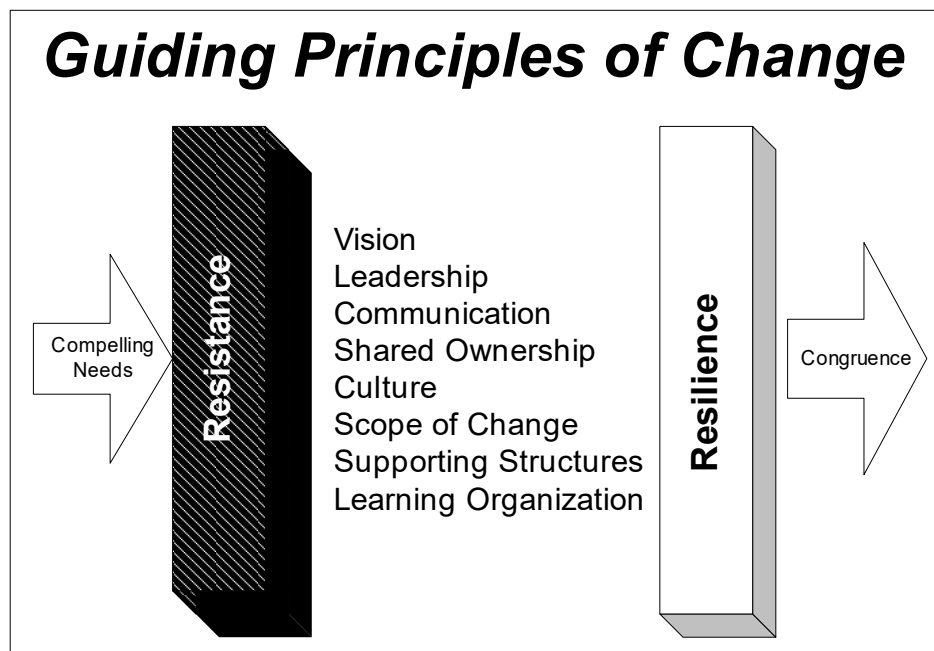

Change Leadership Behaviors

Leaders at all level must participate in the change leadership pattern across the organization. The project team agreed to the following change leadership behaviors:

<Subject>

File Ref: AP020_Project_Team_Orientation_Plan.doc (v. DRAFT 1A)

Company Confidential - For internal use only

Change Leadership Guiding Principles and Roles 16 of 25

Guiding Principles	To Do	How To
Create a Clear, Compelling Vision Give a picture of where you are headed Describe how the vision will be achieved Keep it concise	Promote the project vision and keep in the fore front its tie to the corporate strategy Leaders need to be able to dream and do; get some talented dreamers to help you on the team	Think about how the project can best serve the corporate strategy; dream big. Identify the key benefits of the project. Distill your thoughts from step one and two above: Is there an underlying theme? Aim for elegant simplicity. Figure out where you are now. Spend enough time to know where you are, but your main focus is on the future. Describe the gap in terms of a compelling need to change (This is the transformation.). Try your project vision statement on everyone you meet. If you can't make others understand in less than three minutes, start again.
Assess the Organizational Culture Focus on the customer Look for innovation and creativity Encourage risk taking Evaluate teamwork	Assess your current organizational and team culture. Put the focus of the project squarely on the customer. Create a clear path from the customers' needs to the resources that meet those needs and to the project team. Nurture creativity. Don't punish pioneers.	Assess the organization's readiness to fulfill the project vision. Hold focus groups and gather feedback on how-we-do-things-around-here. Consider benchmarking from the outside. Choose performance measures which tie directly to customer satisfaction. Involve customers; they are key stakeholders in the project; ask for their feedback, and if appropriate, their participation as liaisons to change teams. Ask your team what could be done to allow them to serve the project customers better. Provide opportunities for ideas to surface. Recognize and reward innovation. Recognize some important near misses.
Lead the Way Assemble a coalition Function as a sponsor Serve as role model Create a sense of urgency Endure to the end	Begin with yourself. If you don't role model the future, no one will. Find influential allies who share the project vision. Accelerate the pace just enough to create the right sense of urgency and momentum. Create early wins and communicate those wins. Endure to the end.	Ruthlessly examine yourself to determine how your behavior and approach to the project work, values, plans align with the project vision. Get feedback from others. Wait the talk. Do things highly visible to make the change real. Slay a sacred cow. Assign all on the project team (communication agents) the task of spreading the word throughout the organization. Use hard, cold facts to keep the compelling need for change in plain sight. Set stretch goals. Monitor, measure, celebrate, and set new goals. Cherry pick – find early wins, publicize, reward, celebrate. Give presentations; conduct one-on-ones, focus groups, town hall sessions; preside at celebrations; remove barriers; find resources.

Guiding Principles	To Do	How To
Manage the Scope of Change Stay within people's finite capacity to absorb change Keep an "open system" approach: systems are inter-dependent, multi-dimensional: change one, change all Tie to the vision, to keep the change into context	Assess the people's capacity for change. Lobby to kill, merge or delay any non-essential project. Define the big picture; let people see how initiatives interrelate. Establish strong ties to the corporate strategy.	Review data to inventory current changes and detect people's capacity to absorb change. Gather information on all major projects. Look for objectives, overlaps, conflicts, commonality, scope, and time frames. Help validate the project as priority. Integrate, harmonize remaining projects.
Communicate Openly, Honestly, Relentlessly More is better: Repeat key messages through different sources, consistently Open two way communication channels Manage the information; keep no secrets	Determine your organization's preferred ways of communication. Create a formal plan for two-way communication. Use communication agents. Broadcast successes. Keep abreast of people's needs for communication and meet those needs. Measure the effectiveness of the communication. Manage rumors at their onset.	Create a supportive environment for the communication agents and the two-way communication channels. Use communications (two-way) to: - Create buy-in - Glean ideas you may not have thought of - Build trust - Build enthusiasm - Determine where resistance lies - Estimate the strength of the resistance - Determine the causes of the resistance - Clear up misconceptions - Figure out how far and fast people can move - Make course corrections - Find pockets of support - Surface concerns rather than suppress them
Promote Shared Ownership Involve: People support what they help to create Ownership improves quality and relevancy of decisions: involve everyone, involve them early	Identify your stakeholders. Determine whose support is critical and whose opposition could be dangerous. Find opportunities to create buy-in.	Create a matrix that shows impacted groups and anticipated support levels (Stakeholder matrix). In critical areas, get down to an individual level. Identify their stake in the change. Assess their readiness to change. Hold focus groups with representative sample of highly impacted groups. Hold one-on-one sessions with key stakeholders. Involve stakeholders in supporting the project, ideas generation, focus groups, change teams, communication, and problem solving sessions.
Create Supporting Structures Streamline decision making process Make rewards and recognition supportive of vision Instill measurements tied to the vision Align human resource systems with required behaviors	Keep project bureaucracy to a minimum. Create reward systems specially for the project. Adopt measures to focus on the transformations critical to the project vision. Look for disconnects between HR policies and project set up/vision. Adjust HR systems accordingly.	Keep layers in the project hierarchy to a minimum. Push authority and accountability down. Define the behaviors which are conducive to achieving the project vision. Mix measures; hard, soft, financial, non-financial, process and results. Provide the right learning events. Make participation on the project team a career enhancer.

Guiding Principles	To Do	How To
Build A Learning Organization Operate on an assumption of competence Create safe environment for learning Promote knowledge transfer	Recruit the “best and brightest” Encourage knowledge sharing Promote voluntary followership Unite people behind the project through shared vision, shared values, shared purpose Regard mistakes as learning steps Provide learning opportunities	Encourage individual characteristics which a learning organization should recognize and reward: self-directed learning, respect for others, empathy, curiosity, listening, systems thinking (ability to see how things are interconnected), risk taking, two way communication – dialogue, humility (being teachable), ability to learn from mistakes, self-knowledge – aware of strengths and weaknesses Weave learning through status reporting

Induction Checklist

Each new member to the team will be oriented to the project through the following steps:

Induction Step	Action Items/Information Topics	Documentation/Equipment
Invitation to join the team (one on one conversation with the project lead)	Cover these items in your one-on-one meeting: Role that the new member will play on the team Expertise s/he brings Career opportunity the project provides (what happens to his/her current organizational role) Project vision and business objectives Sponsorship behind project Overview of the project: strategy, implementation decisions, ... Review of Steering Committee and Project Team members Where s/he fits on the project organizational chart; who s/he reports to, who s/he interacts most with Challenges of the project His/her authority level and accountability Performance measures Assign a buddy to provide support to the new team member	Information on the business environment from the proposal Executive Project Strategy (AP.010) Project Orientation Guide (PJM.RM.025) Project management deliverables produced so far
Provide logistical details	Provide equipment Inform about administrative rules Give details on the work site including Office/area, phone Reception phone/fax Access materials, passwords, ... Parking Security badges Work hour ...	Computer Office Supplies Email address/user name Project Accounting Project Numbers Travel expense guidelines Travel agency number Travel profile Employee benefits Employee's book (website address....)
Introduce new member to the team	Introduce the new member to the team members (person to person, during the next meeting, ...) Introduce the new member to the sponsors Review the meeting schedule and identify the meetings the new member needs to attend Review the agenda and required preparation for the next meeting	Roster of all team members with contact information Meeting Agenda Communication Standards and Model
Explain the requirements for communication	Review the communication standards and model for the project team Explain the purpose/importance of communication and status reporting for the team Explain how to use the Project Library	Communication Standards and Model Copies of past Status Reports Project Library documentation
Review the group norms for the team	Emphasize the corresponding behaviors, including change leadership behaviors	Project Team Group Operating Procedures
Prepare the new member to play an active role	Complete the Data Gathering Tool for Project Team Skills Inventory Review/Update learning plan for the team member Schedule learning events and measure effectiveness Update skills sets in member's file Review performance expectations and performance management process	Data Gathering Tool for Project Team Skills Inventory (in Project Team Learning Plan, AP.030) Project team performance management process

Open and Closed Issues for this Deliverable

Open Issues

ID	Issue	Resolution	Responsibility	Target Date	Impact Date

Closed Issues

ID	Issue	Resolution	Responsibility	Target Date	Impact Date

Appendix A - Implementation Team Interview Guide

Implementation Team Insights Interview Questions

1. Do you know what this project is about, that is, vision, expected results, etc.? How does it fit with the corporate strategy? How does it fit with other business initiatives?
2. Do you know why you were selected for the team? What strengths do you bring? How is this assignment perceived?
3. Do you understand your role in the team and how it relates/impacts others? Do you know who all the team members are?
4. What do you hope to get out of this project?
5. What are other projects you have led or in which you played a major role? (dollar amount, time frame, number of people involved, impact on organization, ...)
6. What barriers exist which might hinder the project?
7. What strengths/levers exist which could contribute to the success of the project?
8. What has been the organization's and your past experience in implementing technology? What has gone well? What has not gone well? What ideas do you have for improvement?
9. What is your perception of the sponsorship of this project? (Visibility, commitment, urgency, authority, influence.)
10. How realistic are the goals for the project?
11. How would you evaluate the capability of the project team to achieve the project's goals?
12. What are the communication challenges in the organization?
13. How do you typically get information/updates related to large projects?
14. If you have an urgent message (issue) related to a project, how do you typically communicate it?
15. How would you evaluate the levels of trust within the organization?
16. How much experience have you had in working on cross-functional teams?
17. What perceptions do you have concerning vendor? (The products, the organization, the people)
18. If this project is successful, what benefit will there be for you? For your team? For the organization?
19. How would you evaluate the resistance to this change within the organization?
20. At what sites will the technology be implemented?
21. How many employees at each site? How many users will there be?

22. Is business process design a component of this project? If so, have the process redesigns been completed?

Appendix B - Project Team Performance Measures

Rules of Effective Metrics Program

Three rules need to be followed to have a successful metrics program, temporary or on-going:

1. Measurements must support the business itself. The project measurements must reflect the way in which the project vision supports the corporate strategy.
2. Measurements are not a replacement for management. Measurements are not the "be all and end all," they help communicate and coordinate the project.
3. Measurements must have organizational importance and cannot be considered as overhead.

Approach

The following metrics are refinement of the business value metrics, applied to the project level.

Project Metrics

The following are the metrics the project team selected for measuring the performance of the team throughout the project:

Business Measures	Project Measures	Description
Financial	Cost	Actual project spending compared to budgeted.
Financial	Effort	Hours spent during each project phase and high level activities.
Financial	Schedule	Actual completion of project activities compared to planned project plan.
Financial	Scope Change	Number of approved changes to scope and impact on effort.
Customer	Communication	Adherence to communication metrics from communication strategy.
Customer	Implementation Timeframe	Meet needs of customer during implementation.
Customer	Transition Effectiveness	Impact of transitioning from old system to new system.
Processes	Compliance	Compliance with business drivers (as opposed to doing it to get it done).
Processes	Problem Solving	Number of issues, time to resolve, number outstanding, use of delegated authority, ...
Processes	Staffing	Ability to obtain the proper resources at the right time and project retention rate.
Learning/Improvement	Team Morale	Satisfaction of team members working on the project.
Learning/Improvement	Proficiency	Ability of team members to acquire and use the right skills at the right time.

Business Measures	Project Measures	Description
Learning/Improvement	Communication	Team members receive the timely information they need to fulfill their role.
Learning/Improvement	Change Leadership	Ability of the team leads and members to display the behaviors of effective change leadership

Project Team Performance Tracking

The project team defined as follows the accountability and tracking mechanisms for the team's performance:

Project Measures	Accountability		Tracking Mechanisms		
	Who is accountable?	For what?	Data Source	Frequency	To whom the information is disseminated
Financial					
Cost					
Effort					
Schedule					
Scope Change					
Customer					
Communication					
Implementation Timeframe					
Transition Effectiveness					
Processes					
Compliance					
Problem Solving					
Staffing					
Learning/Improvement					
Team Morale					
Proficiency					
Communication					
Change Leadership					
