

AIM

CV.010 DATA CONVERSION REQUIREMENTS AND STRATEGY

<Company Long Name>

<Subject>

Author: <Author>
Creation Date: May 4, 1999
Last Updated: August 15, 2025
Document Ref: <Document Reference Number>
Version: DRAFT 1A

Approvals:

<Approver 1>

<Approver 2>

ORACLE®

Copy Number _____

Document Control

Change Record

Date	Author	Version	Change Reference
4-May-99	<Author>	Draft 1a	No Previous Document

Reviewers

Name	Position

Distribution

Copy No.	Name	Location
1	Library Master	Project Library
2		Project Manager
3		
4		

Note To Holders:

If you receive an electronic copy of this document and print it out, please write your name on the equivalent of the cover page, for document control purposes.

If you receive a hard copy of this document, please write your name on the front cover, for document control purposes.

Contents

Document Control	ii
Introduction	1
Purpose	1
Project Deliverables Audience	2
Benefits	2
Scope	3
Background	3
Applications	3
Platforms	4
Connectivity	5
Tools	6
Other Technologies	6
Objectives	7
Objectives	7
Critical Success Factors	7
Approach	8
Tasks and Deliverables	8
Key Inputs	9
Constraints and Assumptions	9
Schedule/Critical Milestones	10
Required Resources	10
Conversion Team Organization	10
Roles and Responsibilities	13
Conversion Resource Requirements	14
Conversion Strategy	18
Conversion Approach	19
Automated Tools	21
Conversion Process Flows	22
General Ledger Conversion Process Flow	23
Accounts Receivable Conversion Process Flow	24
Accounts Payable Conversion Process Flow	25
Inventory Conversion Process Flow	26
Bills of Material Conversion Process Flow	27
Work in Process Conversion Process Flow	28
MRP Conversion Process Flow	29
Engineering Conversion Process Flow	30
Purchasing Conversion Process Flow	31

Order Entry Conversion Process Flow	32
Project Standards	33
Century Date Compliance	33
Tool Standards	33
Deliverable Naming Standards.....	34
Data Clean-up Process	35
Data Clean-up	35
Key Data Translations	35
Testing Strategy	36
Acceptance Criteria.....	37
Delivery	37
Data Acceptance	37
Audit/Control.....	37
Issue Tracking Procedures.....	38
Issue Management Procedure.....	38
Issue Resolution	38
Version Control Procedures	39
Change Management	40
Quality Management.....	41
Conversion Requirements	42
Business Object Conversion Selection Criteria	48
Open and Closed Issues for this Deliverable	49
Open Issues.....	49
Closed Issues	49

Introduction

Purpose

This Data Conversion Requirements and Strategy document defines the requirements, scope, objectives, and strategy for the <Project Name> conversion effort.

The Data Conversion Requirements and Strategy document is used as follows:

- The primary use of this document is to record and communicate the data conversion scope, objectives, approach, and requirements.
- The conversion team uses this document to communicate the strategy for successfully converting the legacy data to the new Oracle system(s).
- The conversion team uses this document as a road map for performing the conversion. All members of the team should understand and follow the same strategy.
- The project manager uses this document to understand how the conversion team plans to perform the conversion, and how the conversion effort may impact the overall project.

Distribute and communicate the Data Conversion Requirements and Strategy to the:

- project manager from the implementation services provider
- client project manager, who should sign-off on the conversion requirements and strategy
- conversion team members
- other process leaders who are responsible for tasks that are prerequisites for conversion tasks, or whose tasks are dependent on output from conversion tasks

Use the following criteria to ensure the quality of this deliverable:

- ☐ Are the project scope and objectives clearly identified?
- ☐ Are specific critical success factors documented?
- ☐ Is the impact of each dependent task from other processes considered?
- ☐ Are the conversion requirements clearly defined, including all legacy applications and business objects? Do the definitions indicate the level of detail and history to be converted?
- ☐ Is a disposition path for every existing business object/data element clearly defined?
- ☐ Is the strategy understood by those on the distribution list for this deliverable?
- ☐ Are all assumptions, constraints, and risks that could impact the conversion stated, understood, and mitigated?

Project Deliverables Audience

The conversion activities involve interaction with the following groups:

- <Company Short Name> conversion and interfaces teams
- the project team members responsible for the following conversion prerequisites:
 - Design/Build Standards
 - Existing and proposed System Data Model
 - Database Extension Design
- those responsible for the technical architecture of the overall project conversion and interface capacity requirements
- those responsible for the system test and the systems integration test
- all <Company Short Name> pilot and roll out application and technology installation project teams
- project managers responsible for staffing the conversion and interface effort
- project managers responsible for training project resources

Benefits

By following the proven AIM conversion approach, the following benefits can be realized:

- faster data conversion through defined standards and procedures
- lower conversion cost leveraged from repetitive use of conversion programs
- centralized definition and maintenance of conversion practices, designs, and code
- minimized use of functional and technical resources to repetitively analyze, design, and deploy conversions
- minimized number of resources to support the conversion tasks

Scope

This section identifies included and excluded conversion project scope.

Background

Below is a discussion of the following project features:

- single or multi-site conversion implementation
- single or multi-phased conversion implementation
- single or multiple data sources
- common definition of key data elements across multiple sites
- unique project/legacy system features

Single or Multi-site Conversion Implementation

Single or Multi-phased Conversion Implementation

Single or Multiple Data Sources

Common Definition of Key Data Elements Across Multiple Sites

Common reference date:

Common document data:

Common transaction data:

Common historical data:

Unique Project/Legacy System Features

Applications

This project includes conversion of the following application modules to the defined Oracle Application modules:

<Subject>

File Ref: CV010_Data_Conversion_Requirements_and_Strategy.doc (v. DRAFT 1A)

Company Confidential - For internal use only

Scope 3 of 49

Oracle Application	Checkbox	Documents	Transactions	History
Financials				
General Ledger				
Payables				
Purchasing				
Fixed Assets				
Distribution				
Order Entry				
Receivables				
Inventory				
Manufacturing				
Bills of Material				
Master Scheduling/MRP				
Engineering				
Capacity				
Work in Process				
HR/Payroll				
Project Accounting				
Sales and Marketing				

The following data will be converted to a Data Warehouse:

-
-
-

The following legacy system applications will not be converted in this project to Oracle Applications:

-
-
-

Platforms

Legacy System

The legacy systems currently operate on the following platforms/environment:

Hardware/versions:

-
-
-

Operating system/versions:

-
-
-

Software/versions/module/manufacturer:

-
-
-

Oracle Applications Target System

The Oracle Applications will be running on the following platform/environment:

-
-
-

Connectivity

The following data connectivity/transfer methods are available:

Transparent Gateways

-
-
-

Procedural Gateways

-
-
-

File Transfer Software

-
-
-

PC-Based Transfer Tools

-
-
-

ODBC Drivers

-
-
-

Tools

The following automated tools will be available to facilitate the conversion project:

Data Management Tools

-
-
-

Data Modeling Tools

-
-
-

Data Scrubbing Tools

-
-
-

Data Transformation Tools

-
-
-

Data Mapping Tools

-
-
-

Database Utilities

-
-
-

Other Technologies

The following is a list of third party software to be considered in the scope of this conversion project:

-
-
-

Objectives

Objectives

The key objectives of the conversion effort follow:

- Convert legacy and other related enterprise data to the Oracle Application suite of products.

Critical Success Factors

In addition to the critical success factors that have been identified for the overall Oracle implementation for <Company Short Name>, the following critical success factors are specific to this conversion:

- early conversion planning and coordination across all <Company Short Name> companies to maximize timely and cost-effective enterprise-wide conversion and migration development investments
- well defined technical architecture strategy, requirements, and application configurations that are agreed upon and stable
- participation of representatives from each conversion group as part of the project team helping to ensure consideration of enterprise-wide business and system interface points
- availability of planned Oracle application programmatic interfaces (APIs)
- early identification and completion of key data translations, clean-up, and transformations

Approach

Tasks and Deliverables

The major tasks and corresponding deliverables provided in this conversion project are:

Task	Description	Deliverable
Define Data Conversion Requirements and Strategy	Analyze and document the conversion scope, objectives, approach, requirements, and the strategy for how the conversion will be performed.	Data Conversion Requirements and Strategy
Define Conversion Standards	Document the standards that should be followed throughout the conversion effort.	Conversion Standards
Prepare Conversion Environment	Prepare the conversion environment for the development and testing of the conversion programs.	Conversion Environment
Perform Conversion Data Mapping	Map legacy data files and elements to the Oracle Application table(s) and columns. This map includes an explanation of business, translation, foreign key rules, and default settings.	Conversion Data Mapping
Define Manual Conversion Procedures	Define procedures for manually converting applicable business objects through Oracle Application forms.	Manual Conversion Procedures
Design Conversion Programs	Design how the conversion programs should be coded using conventional programming techniques or built using an automated conversion tool.	Conversion Program Designs
Prepare Conversion Test Plan	Specify test procedures to be followed for performing conversion unit, business object, and validation tests.	Conversion Test Plans
Develop Conversion Programs	Develop conversion programs based on the Conversion Program Design that have been coded or built using an automated conversion tool.	Conversion Programs
Perform Conversion Unit Tests	Test the performance of each of the individual conversion program modules.	Unit-Tested Conversion Programs
Perform Conversion Business Object Tests	Test how the converted data performs within the target application.	Business Object-Tested Conversion Programs
Perform Conversion Validation Tests	Test how the converted data performs within the entire suite of target applications.	Validation-Tested Conversion Programs
Install Conversion Programs	Install the conversion programs that have been coded and tested. If an automated conversion tool is being used, the tool should remain installed until the final conversion is performed	Installed Conversion Programs
Convert and Verify Data	Convert data that has been verified by the users before commencement of production operations.	Converted and Verified Data

Key Inputs

Key inputs to this conversion include:

- Statement of Work
- Documents outlining enterprise application and technology architecture strategy, requirements, and constraints
- Existing and required Business Data Flow
- Application and module configuration including code table definition, Oracle flexfield and descriptive flexfield definition, third-party and custom developed applications key field definitions, etc.
- Module Design Standards
- Module Build Standards
- Existing System Data Model
- Current Process Model
- Trained Users for testing
- Project Management Plan
- Project Workplan
- Project Quality Management Strategies, Standards, and Procedures

Constraints and Assumptions

The conversion effort must operate within the following limits and assumptions:

Time Frames

Resource Availability

Schedule/Critical Milestones

Oracle and <Company Long Name> will review and approve each project milestone by using the standard acceptance criteria for each task deliverable produced.

In addition to the conversion deliverables, the following project milestones have been identified:

Milestone	Phase	Current Conversion Milestone Date	Actual Conversion Milestone Date
Application Installation	Operations Analysis	November 30, 1999	TBD
Configure Applications	Solution Design	December 10, 1999	TBD
Complete legacy data cleanup	Transition	March 31, 2000	TBD

Required Resources

This conversion has the following resource requirements:

- Project Manager
- Client Project Manager
- Business Analyst
- Application Specialist
- Technical Analyst for data mapping and design
- Developer
- IS Manager
- Client Staff Member
- Tester
- Database Administrator
- System Administrator
- User


Conversion Team Organization

The following are the criteria that were used to develop the structure of the conversion team:

- conversion to be completed by <Provide a Date>, in time for Business System Testing
- the number of business objects to be converted
- skills required for conversion

- time estimate for conversion of each business object
- data reconciliation to be done by the users

Based on the above criteria, the conversion team can have one or more groups as shown below.

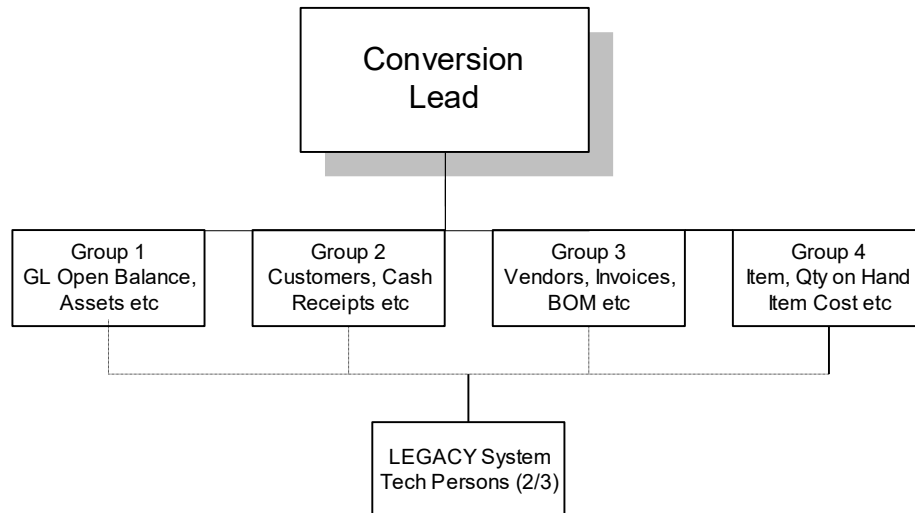

Conversion Group 1

This group will be responsible for the following tasks:

-
-
-

Conversion Group 2

This group will be responsible for the following tasks:

-
-
-

Conversion Group 3

This group will be responsible for the following tasks:

-
-
-

Conversion Group 4

This group will be responsible for the following tasks:

-
-
-

Roles and Responsibilities

The conversion project roles will be staffed by the individuals listed in the table below:

Conversion Group #	Role	Oracle Team Member	Oracle Team Member Position	Client Team Member	Client Team Member Position
	Business Analyst				
	Database Administrator				
	Client Staff Member				
	Developer				
	Technical Analyst				
	User				
	Tester				
	System Administrator				
	Applications Specialist				

Conversion Resource Requirements

The following software and hardware requirements are considered components of this conversion effort:

Software

The application software used as part of this project includes:

Existing Legacy Environment (Source)

-
-
-

Planned Oracle Environment (Target)

-
-
-

Hardware Environment

The hardware and operating software used as part of this project include:

Existing Legacy Environment

-
-
-

Planned Oracle Environment

-
-

Network/File Transport

Existing File Transfer and Network Capabilities

Planned File Transfer and Network Capabilities

Experience/Training Requirements

The staff involved with this conversion must have the background, experience, and training in the following areas:

Task ID	Conversion Task	Background/Experience
CV.010	Define Data Conversion Requirements and Strategy	
CV.020	Define Conversion Standards	
CV.030	Prepare Conversion Environment	
CV.040	Perform Conversion Data Mapping	
CV.050	Define Manual Conversion Procedures	
CV.060	Design Conversion Programs	
CV.070	Prepare Conversion Test Plans	
CV.080	Develop Conversion Programs	
CV.090	Perform Conversion Unit Tests	
CV.100	Perform Conversion Business Object Tests	
CV.110	Perform Conversion Validation Tests	
CV.120	Install Conversion Programs	
CV.130	Convert and Verify Data	

Below is a list of skills that the current conversion project team does not fulfill:

-
-
-

Specialty Tools

The risks associated with the skills that the conversion team does not currently have can be mitigated through training, outside resources, or by using specialty tools.

Below is a list with descriptions of the specialty tools proposed for use on this conversion project:

-
-
-

Business Constraints

This conversion must comply with the following business constraints:

Hardware Availability

-
-
-

Budget Constraints

-
-
-

Legacy System Decommissioning

-
-
-

Technical Standards and Architecture

The project deliverables will be developed subject to:

- any governing <Company Short Name> technology platforms strategy and standards
- decisions made regarding the <Company Short Name> technical architecture plan
- architectural connectivity issues in linking local environments to the central or consolidation environment
- the Technical Architecture (TA) deliverables

Risks and Contingencies

Identified conversion risks include the following:

- incomplete definition of the conversion process
- lack of legacy resources to identify, document, and extract legacy data
- lack of tools to manage/manipulate data
- lack of understanding of project timelines and milestones
- poor data quality
- lack of understanding of required key data translation, clean-up, and transformation criteria
- lack of reliable mechanism for data transfer

The contingency plans that should be put in place for the above risks follow:

-
-
-

Project Metrics

Key metrics for this conversion project follow:


•

- number of platforms:
- number of conversion business objects to design and build:
- number of database tables (may not be known):
- number of conversion modules that can be reused:
- number of source applications to convert from:

- volume of data to be converted and/or migrated:
- complexity of the data to be converted and/or migrated:
- number of legacy data sources:
- amount of required data cleanup:
- number of data translations:

Conversion Strategy

This section provides a graphical description of the conversion approach that will be used to convert the legacy data to the Oracle Applications. An explanation of this strategy follows.

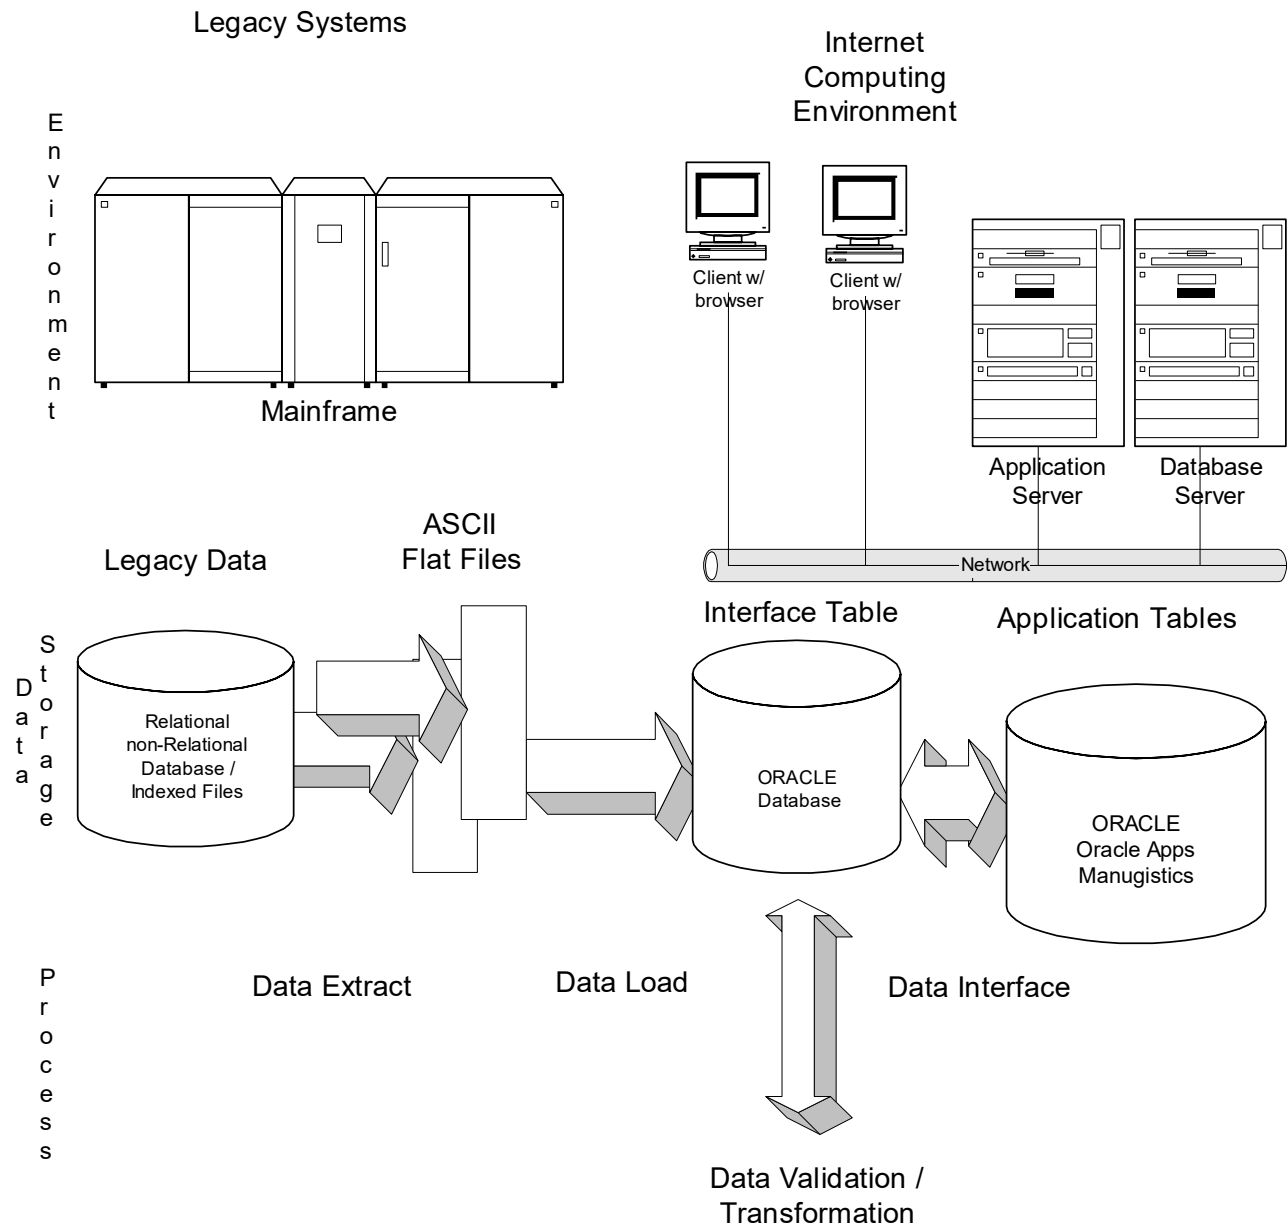

Conversion Approach

1. Conversion Data Mapping

The data mapping process provides detailed lists of the data sets and data elements that will need to be moved into the Oracle tables during the data conversion. During this process, some decisions will need to be made with regard to obtaining information needed by the target application that may not be present in the old system. Default settings, user input, and new data entries are some of the issues that must be addressed during this phase.

The output of this activity is data mapping tables that show what is needed for the Oracle target application processing to meet business operational requirements and where these data elements will come from. Based on this mapping, a design of the legacy data extract is defined.

2. Download Programs

These programs are used to extract the identified conversion data elements from the current systems in the form of an ASCII flat file. The tool that is used to accomplish this task is usually dependent on the abilities and training of the current system programmers. It is important to remember how the flat file will be structured (the order of the records as they are pulled), type of delimitation used, number of records, etc. The flat files must match how the interim tables are set up. The output from a download program is an ASCII flat file as described in the next section.

3. ASCII Flat File

Most database or file systems output data in text form. A comma or space delimited, variable or fixed format data file from the existing system should be generated. If you cannot find a way to produce clean text data, try generating a report to disk, using a text editor to format your data.

One of the outputs of conversion data mapping is to identify the legacy data element data types and precision. After the conversion data mapping is complete, you should know if there are inconsistencies between the legacy data types and the requirements for the Oracle data types. If there are translations that need to take place, these translations can be performed on the legacy system prior to creating the extract or in an interface table. Also, if you are creating a fixed length extract file, you need to take into account the precision level of decimal numbers.

4. Upload Program

Once data has been put into an ASCII EBCDIC flat file and physically moved onto the same computer that has the Oracle RDBMS, the next step is to load the data into a relational database environment.

Programs must be written and run to move data, validate data, and insert/update standard values into default fields. Usually a single loader program is written for each data table being loaded.

5a. Description of Interface Table

The detailed technical description of any interface table that the data is placed into from the ASCII flat file is prepared. An interface table that mimics the production table into which the data will eventually be loaded into should be defined. This allows you to manipulate the data as needed before loading the legacy data into the production tables.

5b. Creation of Interface Table

Before loading the Oracle Application production tables, the legacy data should first be loaded into temporary or interface tables. The interface tables provide a location for you to manipulate and translate the data as needed before validating the data and loading the application production tables. These temporary interface tables need to be built before you run the loader script to populate these tables. The interface tables may be standard Oracle Application interface tables or may be custom interface tables.

6. Translation Programs

These scripts are developed to translate data from the existing system format into useful data for the Oracle target application. An example of this might be taking the date format that exists in the legacy system and converting it into an Oracle format. There may be several or no translation programs, depending on both the type of data coming across and the format of that data.

7. Interface Programs

The interface program scripts are used to populate the production database. The purpose of the interface programs is not only to move the data to the target tables but also to validate the data that would be validated by the form in the target application if the data was converted manually.

8. Application Production Table

This is the final production data table where the converted data resides. These tables are identified early on when doing the initial data mapping. These tables drive some of the translation programs that must ultimately ensure that 100% of the information that the target applications require is present in the final data structures.

9. Testing

This test plan has been integrated into the entire conversion process so that, even during the pre-conversion steps, some type of validation reports are generated from the legacy systems, to be compared later with the converted data.

The approach taken is to use as many standard reports as possible that are available in the legacy and target system for the final data validation. If no reports support the validation requirements, then custom scripts will need to be created for specific validation purposes.

10. Write and Perform Conversion Execution Plan

The conversion execution plan is the execution document that is to be followed when performing the actual conversion. This document is specifically tailored for the <Company Short Name> conversion.

Automated Tools

The following steps within the approach described above will be managed using the automated conversion tool described below:


-
-
-

Conversion Process Flows

When converting specific business objects for a given Oracle application there are business object prerequisites that must be followed. This section contains conversion process flows for the Oracle Applications you are converting that diagram these business object dependencies.

General Ledger Conversion Process Flow


General Ledger Conversion Process Flow Overview

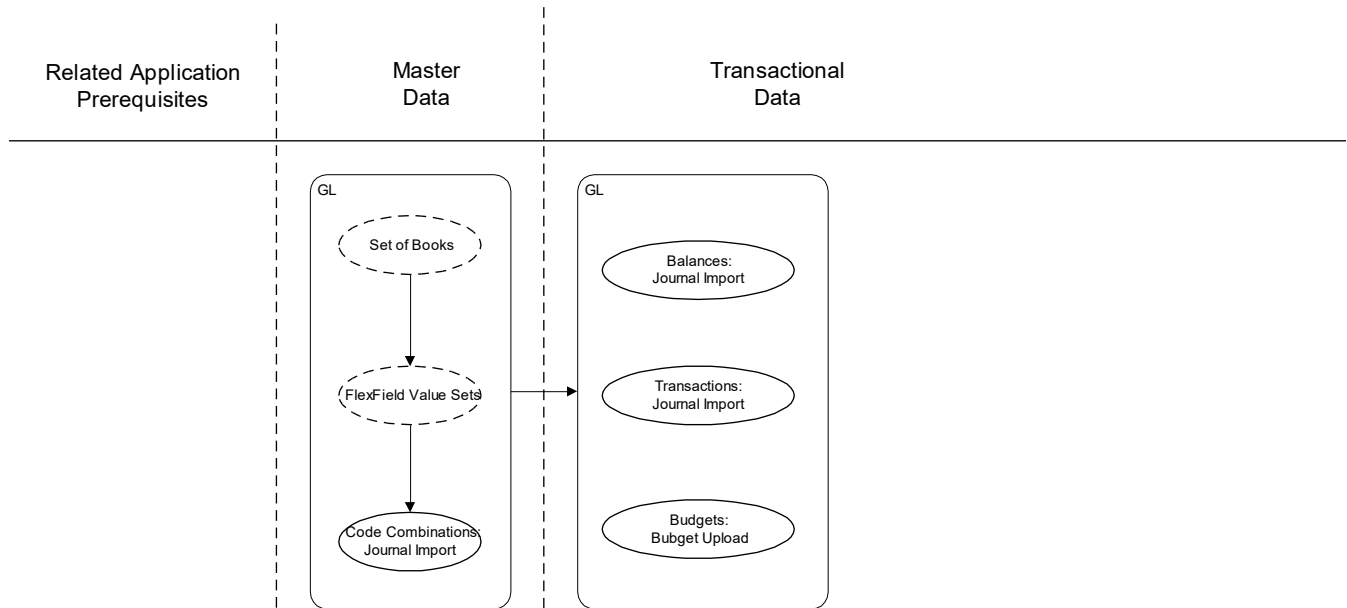


Legend:



Standard Interface




Custom Interface





Application Module

Accounts Receivable Conversion Process Flow

Receivables Conversion Process Flow Overview

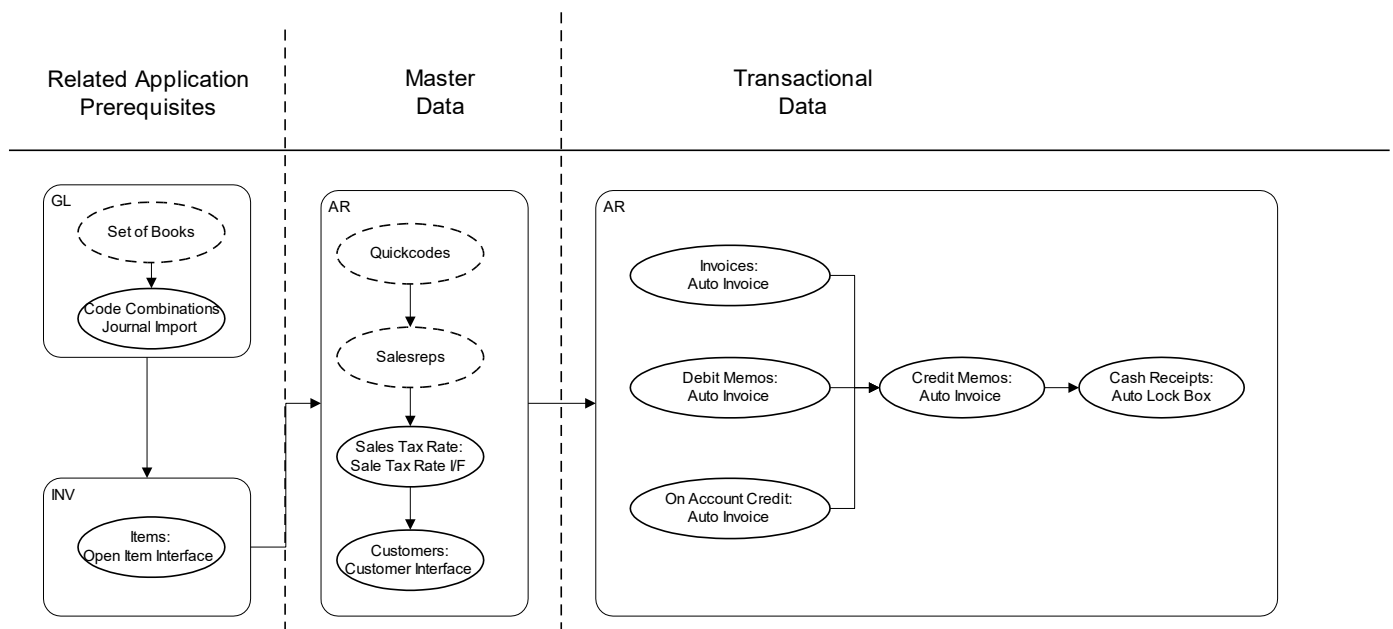


Legend:



Accounts Payable Conversion Process Flow


Payables Conversion Process Flow Overview

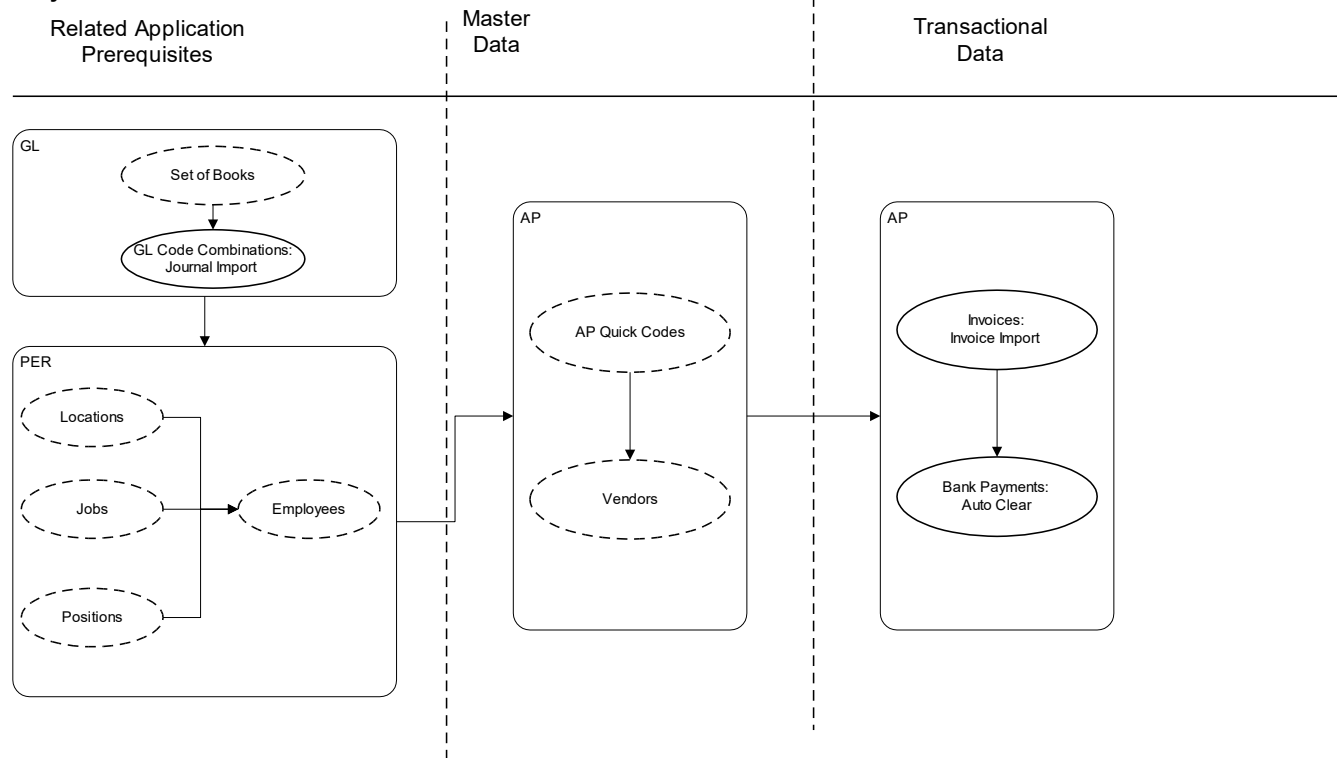


Legend:



Standard Interface



Custom Interface




Application Module

Note : Customers Entity can be implemented either in AR or OE


Inventory Conversion Process Flow

Inventory Conversion Process Flow Overview

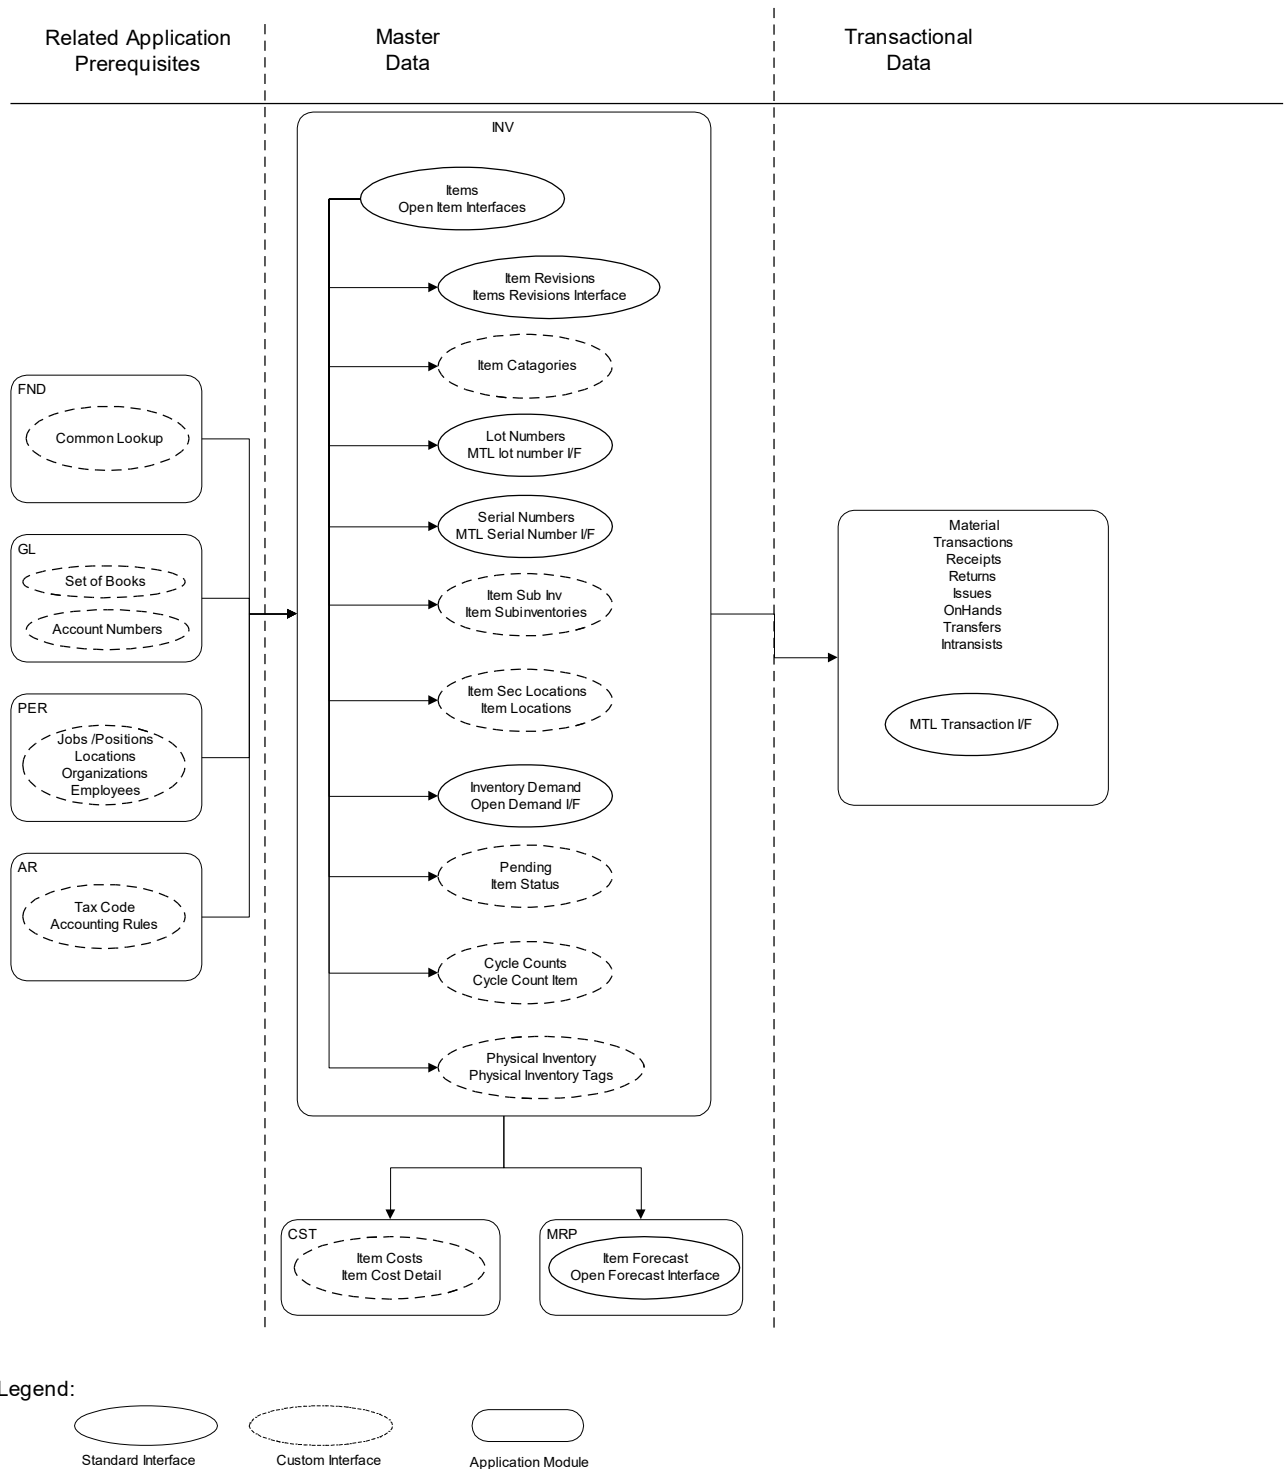

Bills of Material Conversion Process Flow

BOM Conversion Process Flow Overview

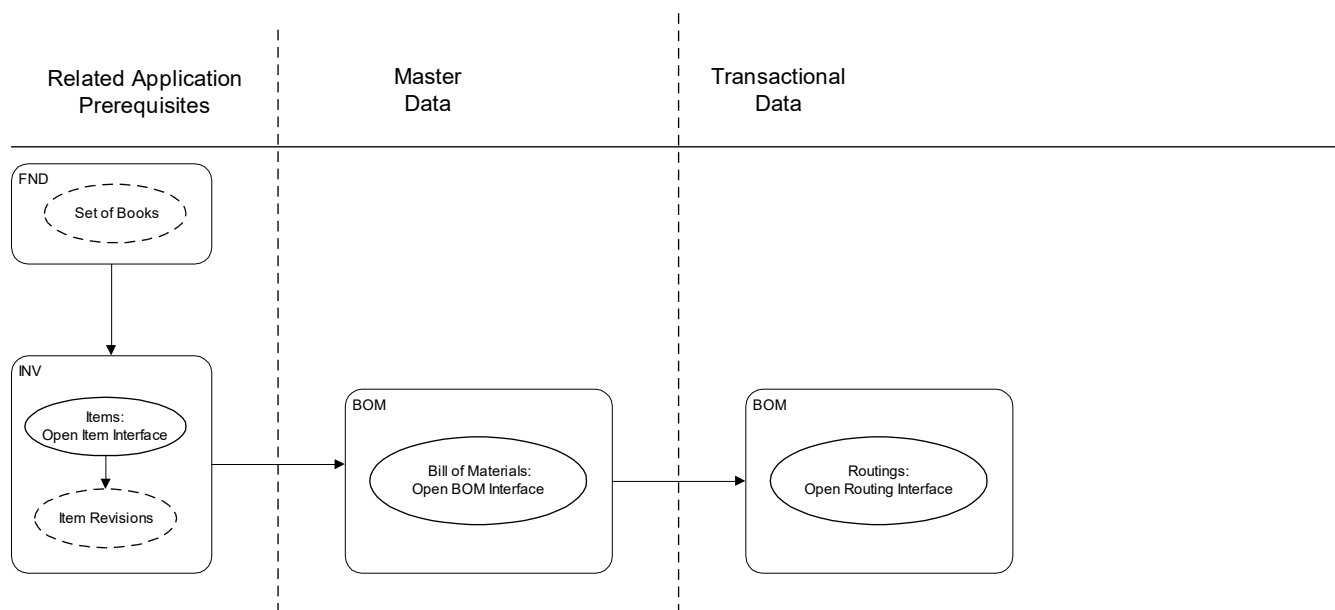

Legend:


Standard Interface

Custom Interface


Application Module

Work in Process Conversion Process Flow

WIP Conversion Process Flow Overview

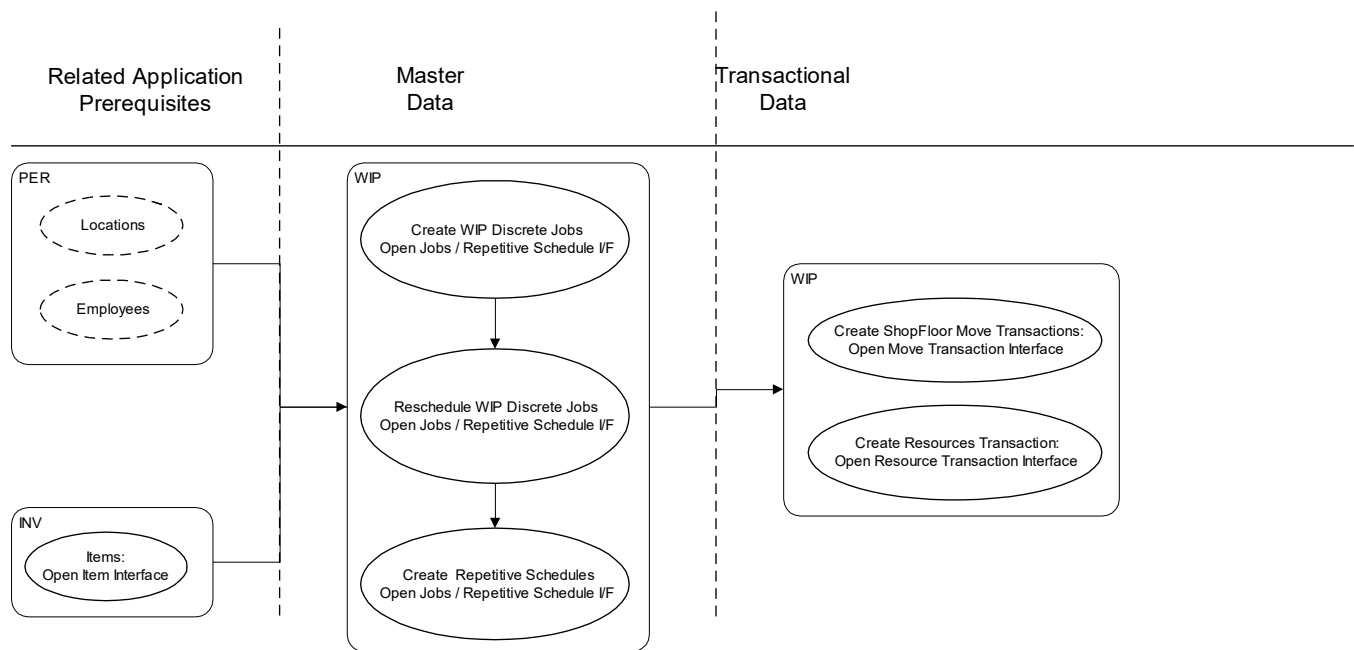


Legend:



MRP Conversion Process Flow

MPS/MRP Conversion Process Flow Overview

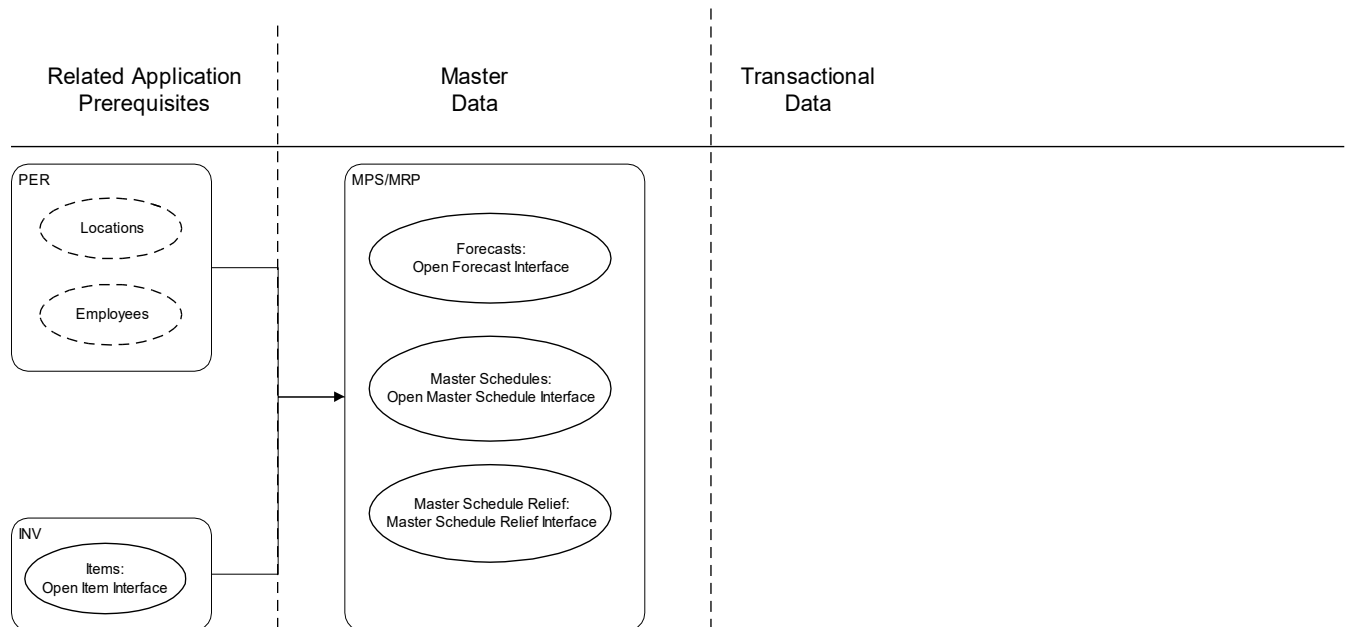


Legend:



Engineering Conversion Process Flow


ENG Process Flow Diagram

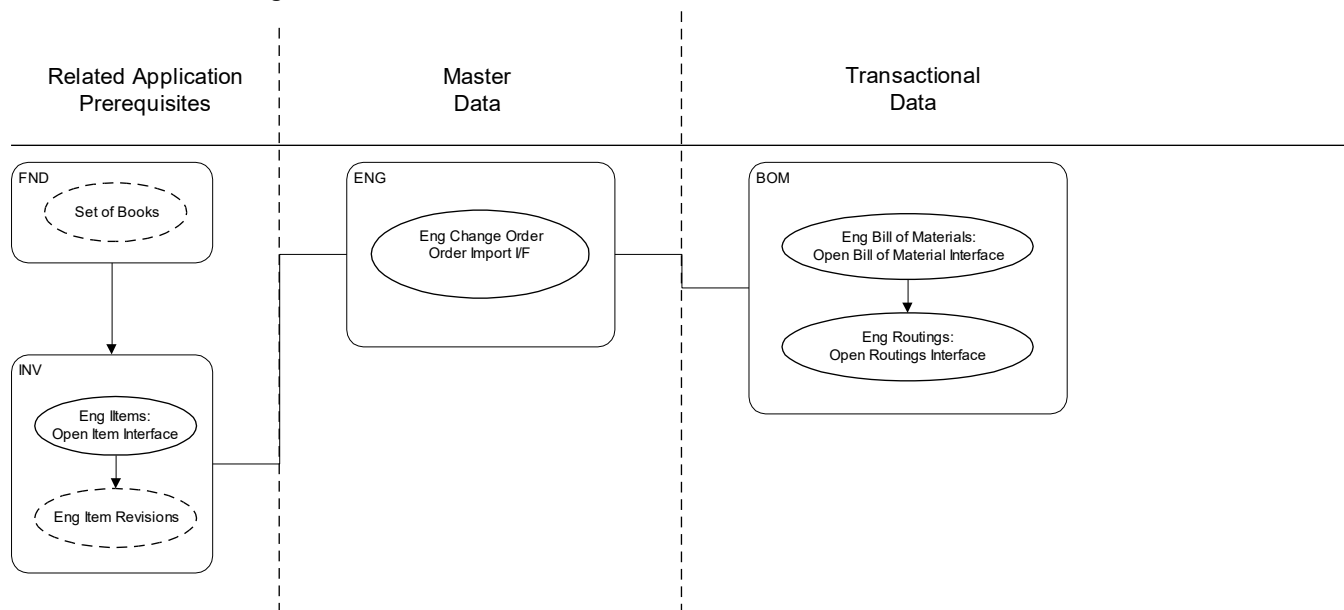


Legend:



Standard Interface




Custom Interface



Application Module


Purchasing Conversion Process Flow

Purchasing Conversion Process Flow Diagram

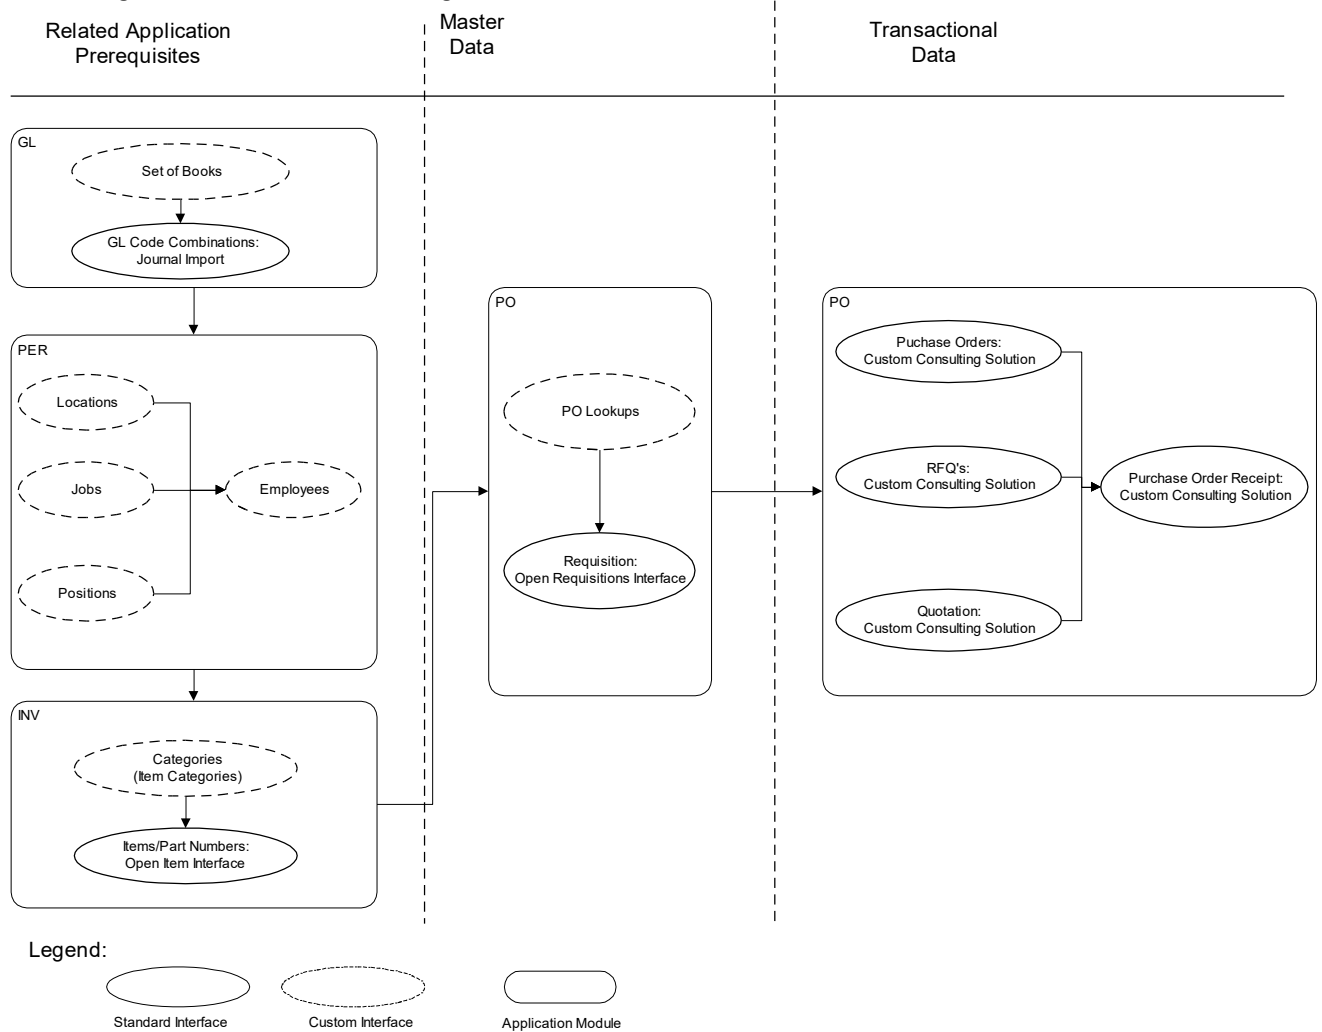

Order Entry Conversion Process Flow

Order Entry Conversion Flow Overview

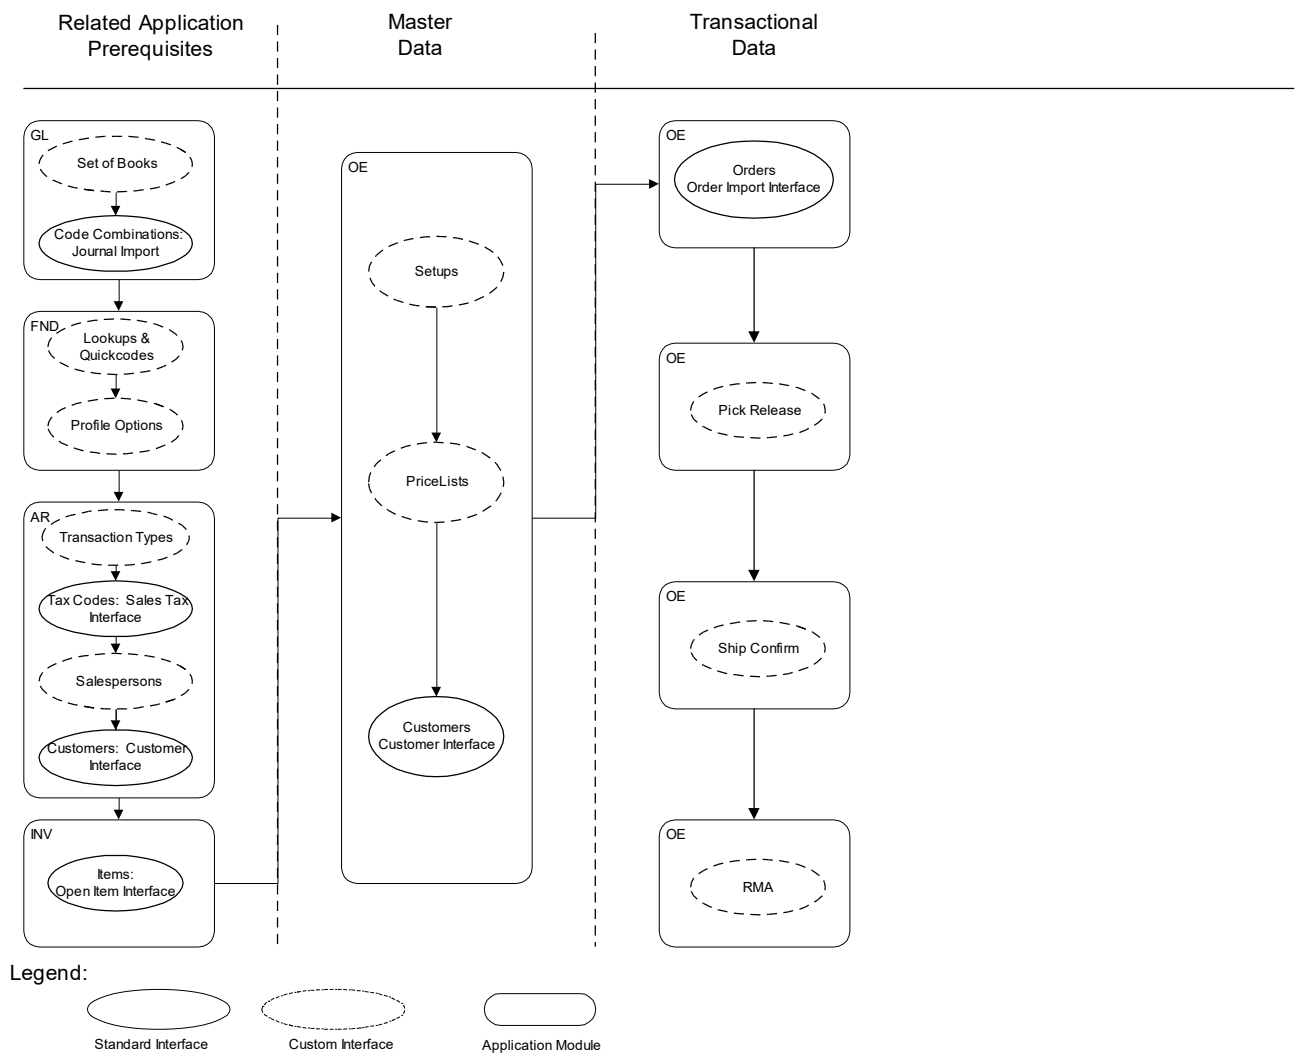

Project Standards

Century Date Compliance

In the past, two character date coding was an acceptable convention due to perceived costs associated with the additional disk and memory storage requirements of full four character date encoding. As the year 2000 approached, it became evident that a full four character coding scheme was more appropriate.

In the context of the Application Implementation Method (AIM), the convention Century Date or C/Date support rather than Year2000 or Y2K support is used. Coding for any future Century Date is now considered the modern business and technical convention.

Every applications implementation team needs to consider the impact of the century date on their implementation project. As part of the implementation effort, all customizations, legacy data conversions, and custom interfaces need to be reviewed for Century Date compliance.

Programmatically converted legacy data must be translated to the appropriate century date state before being uploaded to the production tables. Manually converted legacy data must be keyed into the data entry forms using 4 digits for the year, where supported.

Tool Standards

A list of tool standards specific to the conversion effort follows:

Application Tools

Conversion Tools

Source Control

Version Control

System Management Tools

Deliverable Naming Standards

The following table provides instructions on how to name files, programs, and other project deliverables.

Program Type	Format	Extension	Location/Directory	Example
Upload Module				
Download Module				
Interface Table Creation Module				
Translation Module				
Interface/Conversion Module				
Word Documents				
Other Project Deliverables				

Data Clean-up Process

Data Clean-up

Specific business objects that are candidates for data clean-up include the following:

-
-
-

The strategy for meeting the above data clean-up requirements is as follows:

-
-
-

Key Data Translations

Strategic data that requires translation includes the following business objects:

-
-
-

The strategy for meeting the above data translation requirements is as follows:

-
-
-

Testing Strategy

The agreed upon conversion deliverables should be approved by the client representatives who are responsible for the success of the conversion. In addition, three levels of conversion testing have been identified and described in the Prepare Conversion Test Plans deliverable (CV.070). The following criteria should be considered while performing business object and conversion validation testing:

Application	Business Object	Test Criteria
GL	Summary Balances	Record Counts
		Hash Totals
		Balances
		Journal Debits and Credits

Acceptance Criteria

This conversion's acceptance criteria will be measured by the completion and sign-off of key deliverables as specified in the Project Management Plan [PJM.CR.010, initial complete], produced in task PJM.CR.030. For some projects, these deliverables will be subjected to a quality assurance review.

Each deliverable in the conversion process will be reviewed and approved by the <Company Short Name> representative.

Additionally, each business object conversion may be subject to third-party audit requirements.

Delivery

All conversions will be deemed to be delivered following successful business system testing.

Data Acceptance

Conversion data acceptance criteria should include the following:

- transactability
- ability to reconcile financial information
- definition and acceptance of account level variances

Audit/Control

The audit and control requirements that need to be met are listed below:

-
-
-

Issue Tracking Procedures

Issue Management Procedure

All conversion issues will be tracked and managed as part of the overall project-level implementation process.

Issue Resolution

All conversion issues will be resolved using the project issue resolution process.

Version Control Procedures

All versions of instance information and conversion modules will be managed under version/source control. The version source control strategy being used by the overall project will be followed. Specific conversion version control standards are discussed in the deliverable Conversion Standards (CV.020).

Change Management

The scope and objectives of this conversion will be strictly controlled using the Oracle Project Management Method (PJM). A detailed discussion of change management is found in the Quality Management Strategies, Standards, and Procedures (PJM.QM.010). Change management should be adopted at the overall project level. Therefore, the conversion should use the same change management guidelines used by each of the other AIM processes.

The following change management procedures will be followed:

- identify scope definition change
- review the identified scope change with management
- analyze the impact of the scope change on the schedule and conversion project estimate
- review the scope change and obtain approval from overall project manager
- incorporate the scope change into the project workplans and budgets

Scope changes may be addressed and formalized for any of the reasons below:

- delayed delivery of legacy data extracts
- increased requirements for data-cleanup
- increased need for data translations between legacy data and target application data
- delayed receipt of application code
- delayed change in accounting flexfield structure and segment values

Quality Management

It is part of the Quality Management Strategies, Standards, and Procedures (PJM.QM.010) scope to determine the governing quality system that will be in effect for its deliverables and to define quality management procedures in detail to satisfy the requirements of the quality system.

At a minimum, an independent quality review will be provided to address two fundamentally different aspects of project activities:

- quality, completeness, and appropriateness of the project deliverables
- quality, completeness and appropriateness of project management, practices, and procedures

The review participants are expected to be designated by both <Company Short Name> and Oracle in accordance with the detailed quality procedures developed by the overall project.

Conversion Requirements

Disposition Type:

- M= Manual
- P= Programmatic
- A= Archival

Business Object Type:

- R= Reference
- D= Document
- T= Transaction
- H= Historical
- A= Aggregation/Roll-up

Business Ranking:

- M= Mandatory
- R= Preferred
- O= Optional
- W= Wish List
-

(1)	(2)	(3)	(4)	(5)	(6)	(7)	(8)	(9)
Application Module	Sequence to be Converted	Business Object & Business Object Type	Business Ranking	Disposition Type	Data Volumes/ Number of Legacy Sources	Frequency: One Time/ Periodic	Standard Oracle Open Interface	Comments/Open Issues
GL	1	Account Valid Values						
	2	Code Combinations					Journal Import	

(1)	(2)	(3)	(4)	(5)	(6)	(7)	(8)	(9)
Application Module	Sequence to be Converted	Business Object & Business Object Type	Business Ranking	Disposition Type	Data Volumes/ Number of Legacy Sources	Frequency: One Time/ Periodic	Standard Oracle Open Interface	Comments/Open Issues
	3	Journal Entries					Journal Import	
	4	Balances-: Summary					Journal import	
	5	Balances: Detail					Journal Import	
	6	Budgets					Budget Upload	
PO	1	Employees/ Buyers						
	2	Vendors						
	3	Items					Open Item Interface	
	4	Purchase Agreements						
	5	Quotations						
	6	Requisitions					Requisitions Interface	
	7	Purchase Orders (Open)						
	7	Purchase Orders (Closed)						
	8	Receipts						
AP	1	Employees						
	2	Bank Accounts						
	2	Vendors						
	4	Invoices (Open)					Invoice Import	
	4	Invoices (Closed)					Invoice Import	
	5	Payments						
	5	Prepayments						
	6	Notes						
FA	1	Mass Additions					Mass Additions Interface	
	2	Production					Production Interface	
	3	Budgets					Budget Interface	
AR	1	Salespersons						
	1	Tax Codes & Rates						
	1	Banks						
	1	Sales Tax Rates					Sales Tax Rate Interface	
	1	Exchange Rate Adjustments						

(1)	(2)	(3)	(4)	(5)	(6)	(7)	(8)	(9)
Application Module	Sequence to be Converted	Business Object & Business Object Type	Business Ranking	Disposition Type	Data Volumes/ Number of Legacy Sources	Frequency: One Time/ Periodic	Standard Oracle Open Interface	Comments/Open Issues
	2	Customers					Customer Interface	
	3	Invoices: Open					AutoInvoice	
	3	Invoices: Closed					AutoInvoice	
	3	Invoices: Partially paid					AutoInvoice	
	3	Commitments						
	4	Credit Memos					AutoInvoice	
	4	Debit Memos					AutoInvoice	
	4	On-Account Credit					AutoInvoice	
	5	Cash Receipts					AutoLockbox	
	6	Invoice Adjustments						
OE	1	Items					Open Item Interface	
	1	Price Lists						
	1	Salespersons						
	1	Tax Locations and Rates						
	2	Customers					Customer Interface	
	3	Sales Orders (Open)					Order Import	
	3	Sales Orders (Closed)					Order Import	
	4	Sales Order Notes						
	5	Return Material Authorization						
	6	Pick Release						
INV	1	Subinventories						
	1	Locators						
	2	Items					Open Item Interface	
	3	Inventory Receipts					Open Transactions Interface	
	3	Returns and Adjustments					Open Transactions Interface	
	3	Item Revisions						
	3	Item Replenishment					Open Replenishment Interface	
	3	Item Costs						

(1)	(2)	(3)	(4)	(5)	(6)	(7)	(8)	(9)
Application Module	Sequence to be Converted	Business Object & Business Object Type	Business Ranking	Disposition Type	Data Volumes/ Number of Legacy Sources	Frequency: One Time/ Periodic	Standard Oracle Open Interface	Comments/Open Issues
	3	Item Demand					Open Demand Interface	
	3	On-hand Quantities					Open Transaction Interface	
BOM	1	Resources						
	1	Locations						
	1	Departments						
	1	Alternates						
	2	Bills of Material					Bill of Material Interface	
	3	Routings					Routings Interface	
Master Scheduling/ MRP	1	Employees						
	2	Forecasts					Open Forecast Interface	
	3	Master Schedule Entries					Open Master Schedule Interface	
	4	Master Schedule Relief					Master Schedule Relief Interface	
ENG	1	Employees						
	2	ECO Departments						
	3	Engineering Items					Open Item Interface	
	4	Eng. Item Revisions						
	5	Item Cross Reference						
	6	Engineering Change Notice						
	7	Eng. Item BOM					Bill of Material Interface	
	8	Eng. Routing					Routings Interface	
Capacity	1	Bill of Resources						
	2	Bill of Resource Sets						
WIP	1	Resources					Open Resource Transaction Interface	
	2	Material (Serial Numbers & Lot Numbers)					Material Transaction Interface/ Serial Number Interface and Lots Interface	If you are using serial number or lot number control then use the Serial Number and / or Lot Number Interface.
	2	WIP Floor Transactions					Open Move Transactions	

<Subject>

Conversion Requirements 45 of 49

(1)	(2)	(3)	(4)	(5)	(6)	(7)	(8)	(9)
Application Module	Sequence to be Converted	Business Object & Business Object Type	Business Ranking	Disposition Type	Data Volumes/ Number of Legacy Sources	Frequency: One Time/ Periodic	Standard Oracle Open Interface	Comments/Open Issues
							Interface	
	2	WIP Material Transactions					Open Move Transactions Interface	
	2	WIP Completion Transactions					Open Move Transactions Interface	
	3	Discrete Jobs					Open Job and Repetitive Schedule Interface	
	4	Repetitive Schedules					Open Job and Repetitive Schedule Interface	
Projects	1	Project Templates						
	2	Projects						Capital, Contract, and Indirect Projects
	3	Tasks						
	4	Budgets						Cost and Revenue Budgets
	5	Agreements						
	6	Funding						
	7	Expenditures						
	8	Revenue						
	9	Invoices						
HR/Payroll	1	Locations						
	2	Organizations						
	3	Jobs						
	4	Grades						
	5	Positions						
	6	Employees						
	7	Positions						
	8	Pay Elements						
	9	Pay Elements History						
	10	Deductions						
	11	Deductions History						
Oracle Sales & Marketing		Sales Force						
		Companies						Prospects and Customers

(1)	(2)	(3)	(4)	(5)	(6)	(7)	(8)	(9)
Application Module	Sequence to be Converted	Business Object & Business Object Type	Business Ranking	Disposition Type	Data Volumes/ Number of Legacy Sources	Frequency: One Time/ Periodic	Standard Oracle Open Interface	Comments/Open Issues
		Company Contacts						
		Events						
		Event Facilities						
		Collateral						Product Literature
		Advertisements						
		Sales Territories						
		Action Items						
		Marketing Programs						
		Mail or Call Scripts						
		Letters						Cover letters to send with product literature
		Forecasts						

Business Object Conversion Selection Criteria

Define the selection criteria for each of the business objects that are being converted as identified in the Conversion Requirements table in the previous component.

The selection criteria are:

- Historical/ Active Periods
- Date Ranges
- Active/Obsolete
- Acquired/Dissolved/Sold-off
- Number of Periods

Business Object	Selection Criteria
AP Invoices	Open (Unpaid) status only

Open and Closed Issues for this Deliverable

Open Issues

ID	Issue	Resolution	Responsibility	Target Date	Impact Date

Closed Issues

ID	Issue	Resolution	Responsibility	Target Date	Impact Date
